PHASE I

NOTES:

1. *ALL TEMPORARY TRAFFIC CONTROL WORK SHALL CONFORM TO THE LATEST EDITION OF THE "MANUAL ON UNIFORM TRAFFIC CONTROL DEVICES" (MUTCD) AND ALL REVISIONS, UNLESS SUPERCEDED BY THESE PLANS.*
2. *ALL SIGN LEGENDS, BORDERS, AND MOUNTING SHALL BE IN ACCORDANCE WITH THE MUTCD.*
3. *TEMPORARY CONSTRUCTION SIGNING AND ALL OTHER TRAFFIC CONTROL DEVICES SHALL BE IN PLACE PRIOR TO THE START OF ANY WORK.*
4. *TEMPORARY CONSTRUCTION SIGNING, BARRICADES, AND ALL OTHER NECESSARY WORK ZONE TRAFFIC CONTROL DEVICES SHALL BE REMOVED FROM THE HIGHWAY OR COVERED WHEN THEY ARE NOT REQUIRED FOR CONTROL OF TRAFFIC.*
5. *SIGNS AND SIGN SUPPORTS LOCATED ON OR NEAR THE TRAVELED WAY, CHANNELIZING DEVICES, BARRIERS, AND CRASH ATTENUATORS MUST PASS THE CRITERIA SET FORTH IN NCHRP REPORT 350, "RECOMMENDED PROCEDURES FOR THE SAFETY PERFORMANCE EVALUATION OF HIGHWAY FEATURES" AND/OR "MANUAL FOR ASSESSING SAFETY HARDWARE" (MASH).*
6. *CONTRACTORS SHALL NOTIFY EACH ABUTTER AT LEAST 24 HOURS IN ADVANCE OF THE START OF ANY WORK THAT WILL REQUIRE THE TEMPORARY CLOSURE OF ACCESS, SUCH AS CONDUIT INSTALLATION, EXISTING PAVEMENT EXCAVATION, TEMPORARY DRIVEWAY PAVEMENT PLACEMENT, AND SIMILAR OPERATIONS.*
7. *THE FIRST TEN PLASTIC DRUMS OF A TAPER SHALL BE MOUNTED WITH TYPE A LIGHTS.*
8. *THE ADVISORY SPEED LIMIT, IF REQUIRED, SHALL BE DETERMINED BY THE ENGINEER.*
9. *DISTANCES ARE A GUIDE AND MAY BE ADJUSTED IN THE FIELD BY THE ENGINEER.*
10. *MAXIMUM SPACING OF TRAFFIC DEVICES IN A TAPER (DRUMS OR CONES) IS EQUAL IN FEET TO THE SPEED LIMIT IN MPH.*
11. *MINIMUM LANE WIDTH IS TO BE 11 FEET (3.3m) UNLESS OTHERWISE SHOWN. MINIMUM LANE WIDTH TO BE MEASURED FROM THE EDGE OF DRUMS OR MEDIAN BARRIER.*
12. *ALL SIGNS SHALL BE MOUNTED ON THEIR OWN STANDARD SIGN SUPPORTS.*

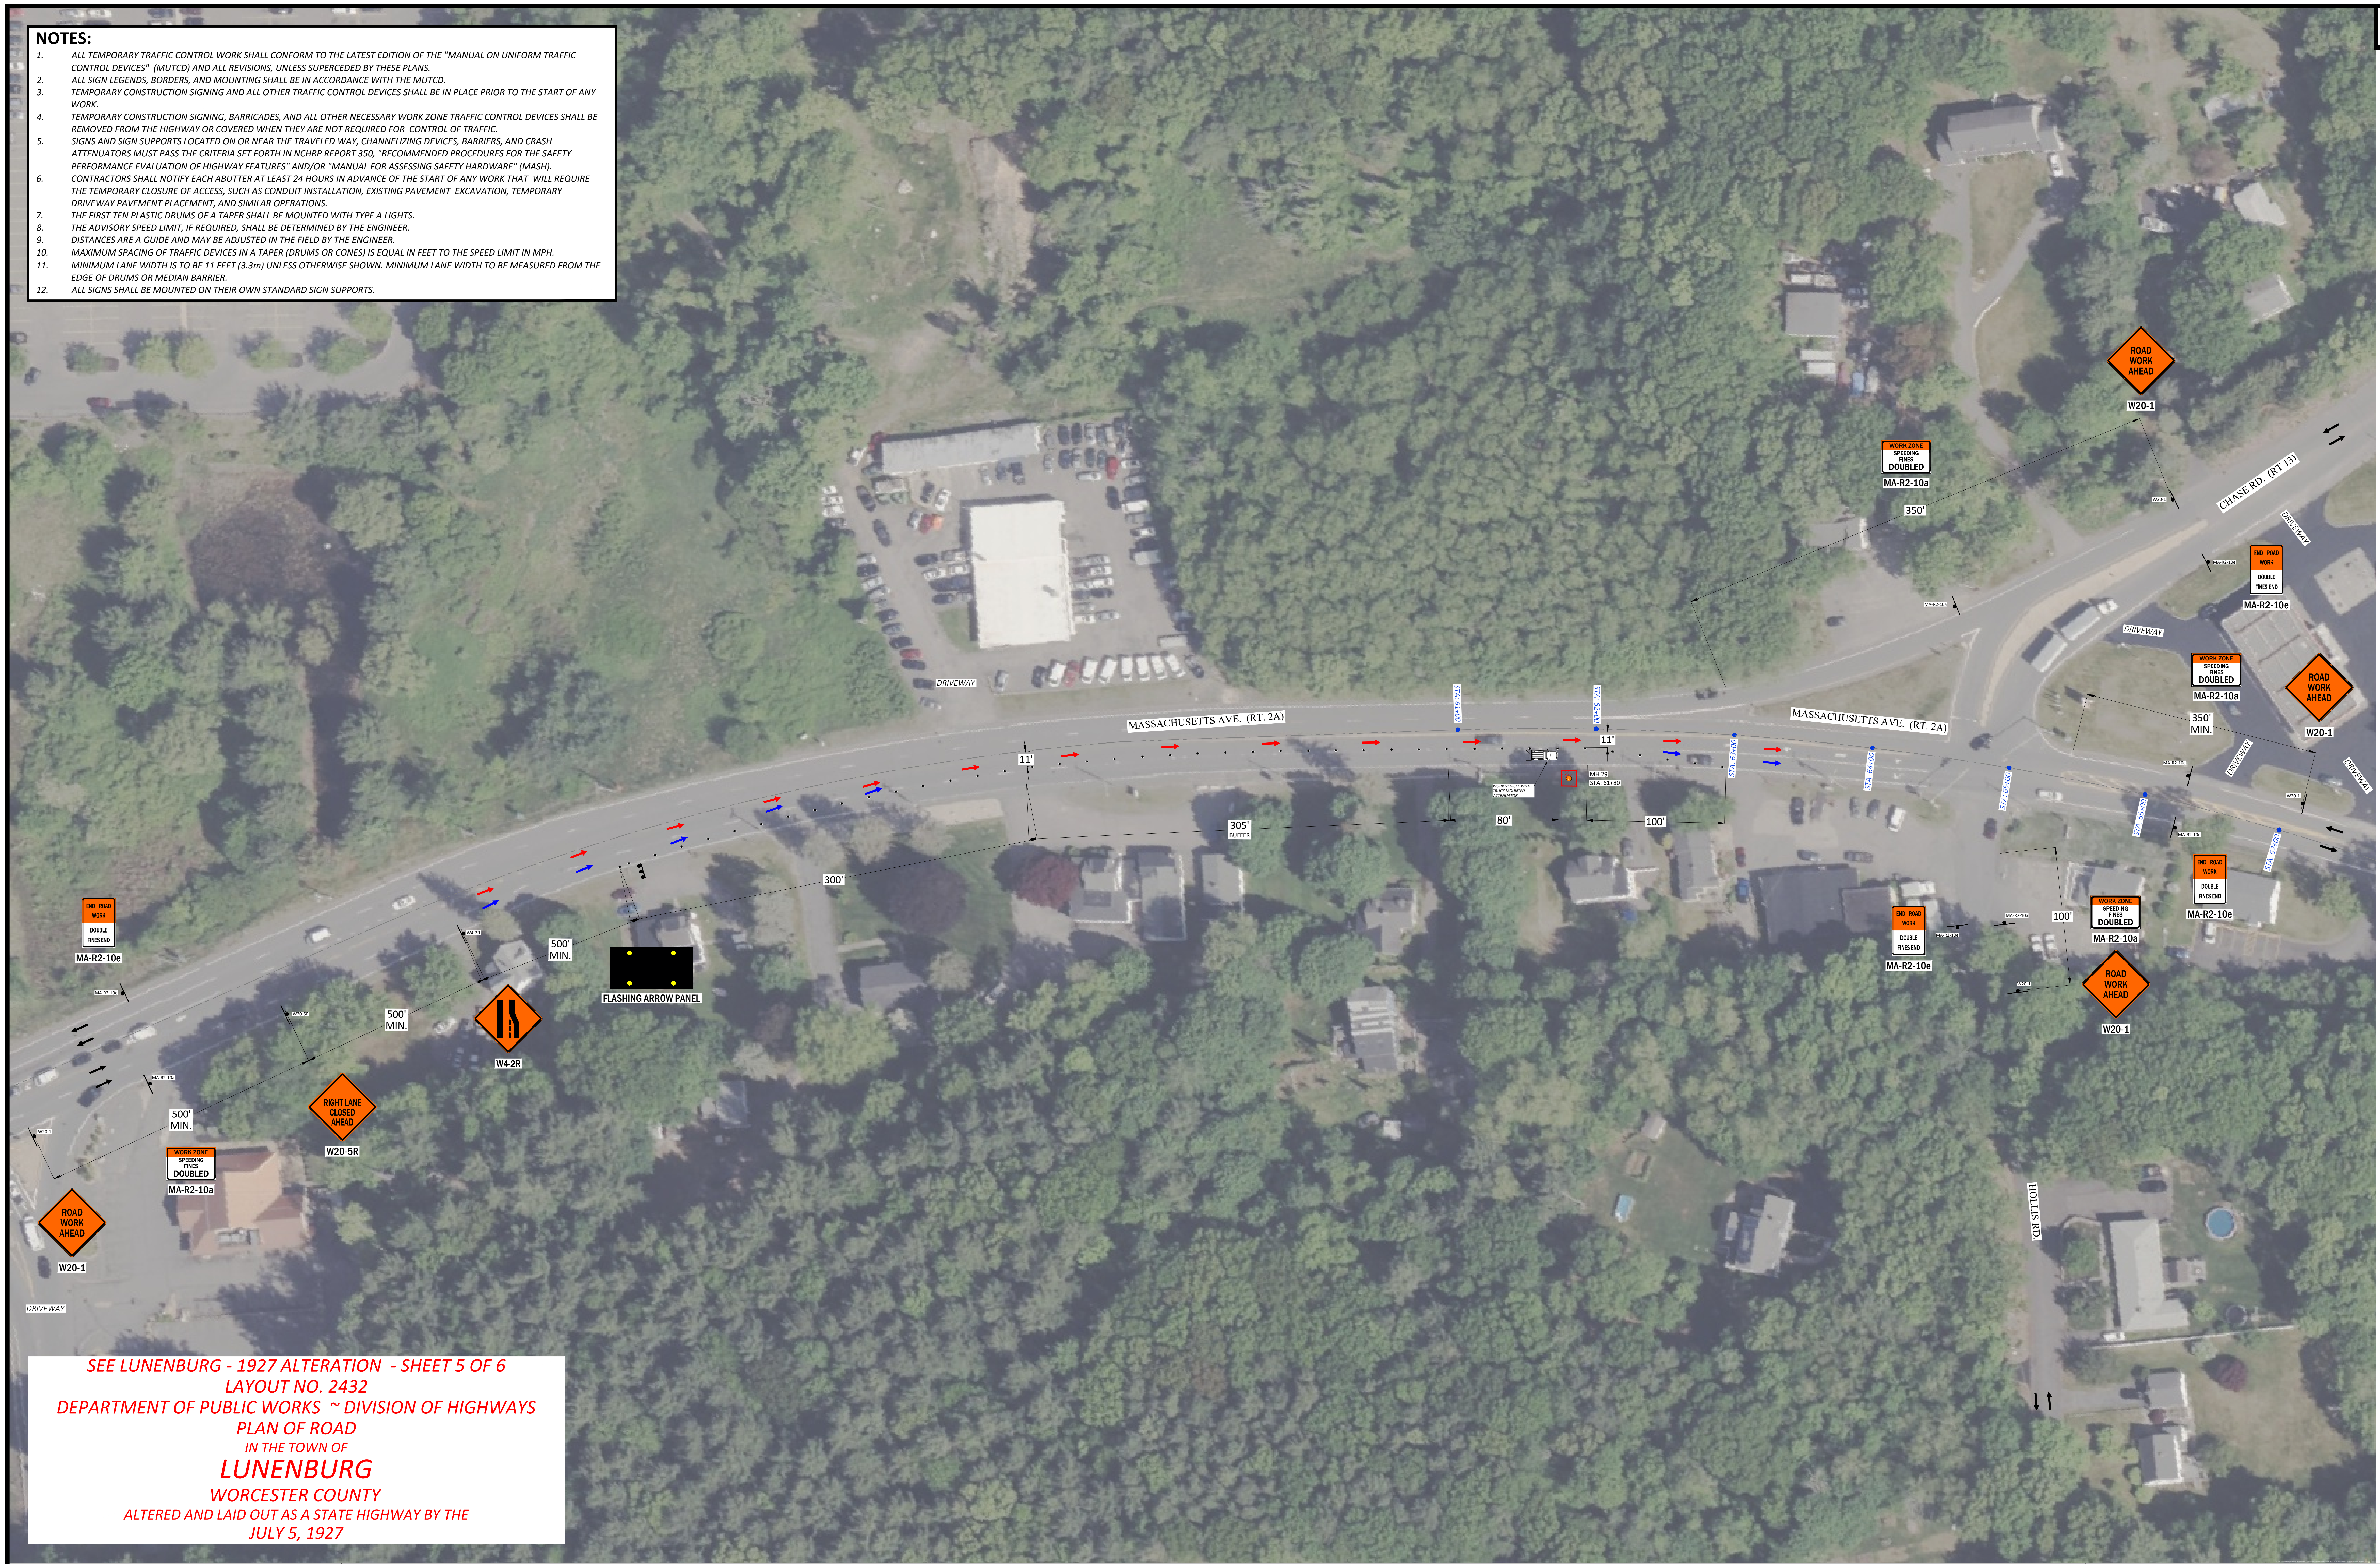

SEE LUNENBURG - 1927 ALTERATION - SHEET 5 OF 6
LAYOUT NO. 2432
DEPARTMENT OF PUBLIC WORKS ~ DIVISION OF HIGHWAYS
PLAN OF ROAD
IN THE TOWN OF
LUNENBURG
WORCESTER COUNTY
ALTERED AND LAID OUT AS A STATE HIGHWAY BY THE
JULY 5, 1927

TRAFFIC LEGEND	
▨	WORK ZONE
- - - - - - - -	PROPOSED TRENCH
■	CHANNELIZING DEVICE (CONE)
◉	CHANNELIZING DEVICE (BARREL)
┤	SIGN
POLICE	POLICE DETAIL
⊖	SINGLE PARKING METER
⊖⊖	DOUBLE PARKING METER
V	VARIABLE MESSAGE BOARD
●●●	ARROW BOARD
▨	TYPE 3 BARRICADE
✱	HIGH LEVEL WARNING DEVICE
▭	CONSTRUCTION TRUCK
◸	TRUCK MOUNTED ATTENUATOR
←	1 WAY STREET
⇄	2 WAY STREET
↔	2 WAY TRAFFIC (WORK ZONE)
←	TRAFFIC FLOW (WORK ZONE)
←	TRAFFIC FLOW (WORK ZONE)
←	TRAFFIC FLOW (WORK ZONE)
(T)	EXISTING MBTA BUS STOP
Ⓣ	RELOCATED MBTA BUS STOP

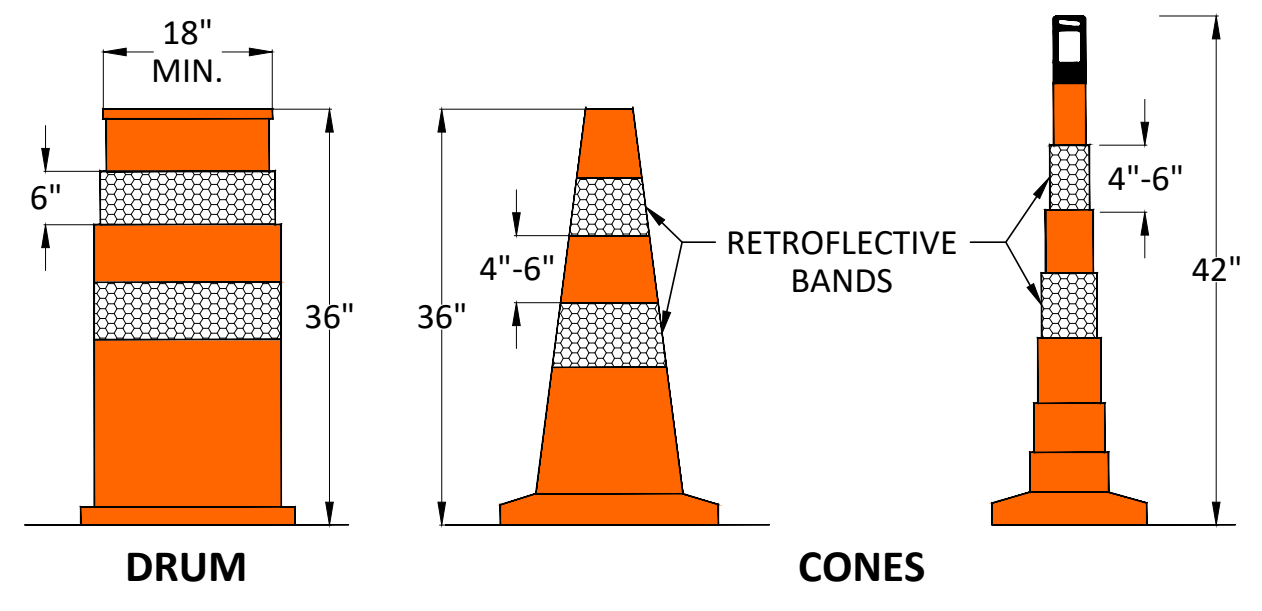

CHANNELIZATION DEVICE DETAIL
TYPICAL
NOT TO SCALE

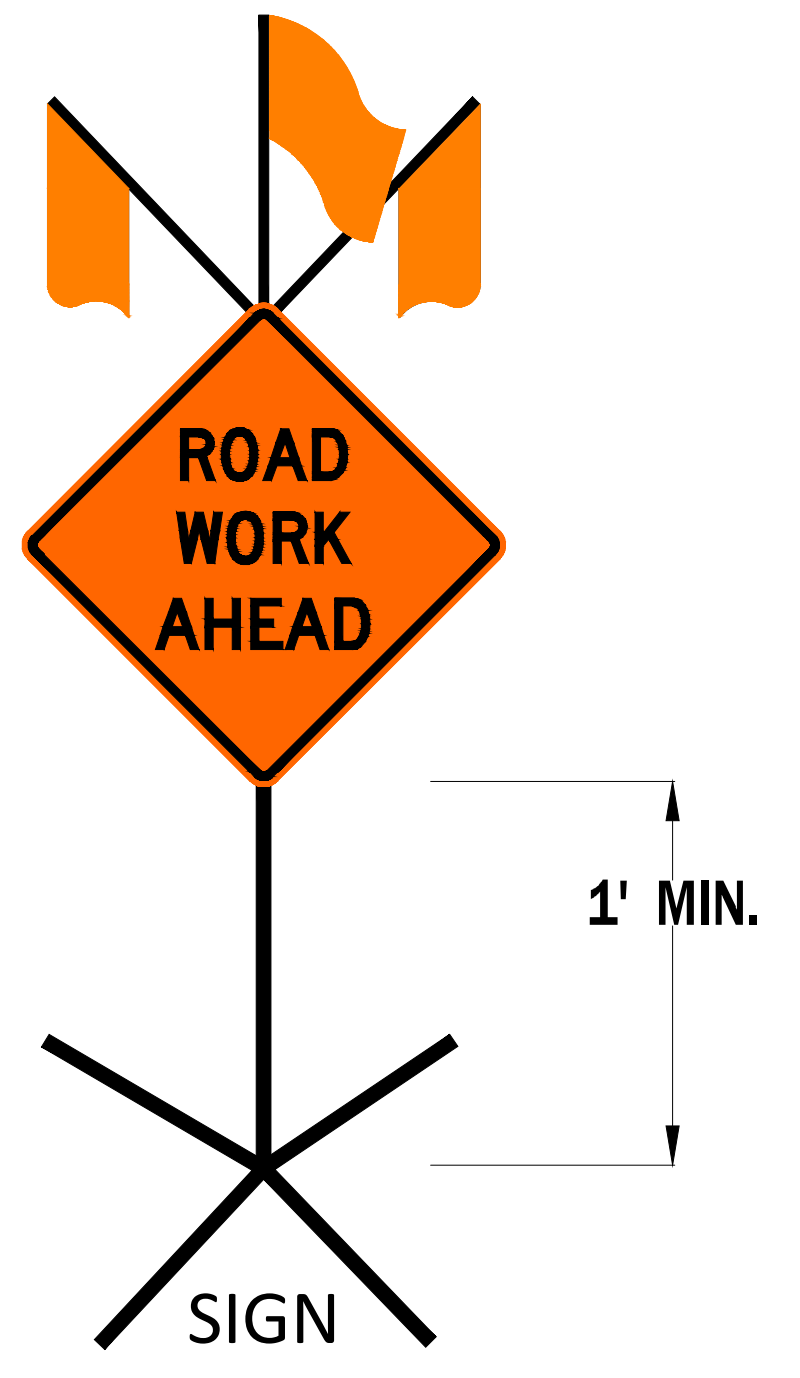

FREE STANDING
SELF SUPPORT SIGN
(TYPICAL)
(NOT TO SCALE)

PAGE 792
PER SEC. 6F.03
MUTCD 11th EDITION
DECEMBER 2023

REVISIONS		
REV	DESCRIPTION	DATE
--	---	---

NOTE:
EXISTING UTILITIES SHOWN ARE APPROXIMATE AND NOT WARRANTED TO BE CORRECT. THE CONTRACTOR SHALL VERIFY THE LOCATION OF ALL PUBLIC AND PRIVATE UTILITIES PRIOR TO BEGINNING ANY EXCAVATION.

811 DigSafe MA·ME·NH·RI·VT

KNOW WHAT'S BELOW
CALL BEFORE YOU DIG
IT'S FREE AND IT'S THE LAW

CALL 811 OR 1-888-DIG-SAFE

NOTES:

- SPEED LIMIT 40 MPH AS NOTED ON THE massDOT ONLINE ROAD INVENTORY.
- SIDEWALKS NOT PRESENT ON EITHER SIDE OF MASSACHUSETTS AVE. (ROUTE 2A), ADJACENT TO THE WORK ZONE.
- ALLOW BREAKS IN CHANNELIZATION DEVICES TO PERMIT DRIVEWAY ACCESS.

SCALE:

1"= 60 FEET
0 60 120 180 240

massDOT
Massachusetts Department of Transportation

PREPARED BY:

PIKE TELECOM
21 Oxford Rd
Mansfield, MA 02048
www.piketelecom.com
1-508-337-7600

PREPARED FOR:

verizon

TITLE:

TRAFFIC MANAGEMENT PLAN - PHASE I
410-603 MASSACHUSETTS AVE. (RT 2A & RT 13)
LUNENBURG, MA 01462

SURVEYED BY: PIKE TELECOM	PRINT NO: 1 OF 3
DRAWN BY: MPO	SCALE: 1" = 60
DATE: 09/30/26	EWO: 1A8P1SA WPI 3167248

09/30/2026 N:\CADD\VERIZON BAU TMP\2026\AA - TMP\BB - TMP - MA\1A8P1SA WPI 3167248 - 410-603 MASS AVE (RT 2A) - LUNENBURG - massDOT TMP\AA - AUTOCAD\1A8P1SA WPI 3167248 - 410-603 MASS AVE (RT 2A) - LUNENBURG - massDOT TMP.dwg

017850300410217

PHASE II

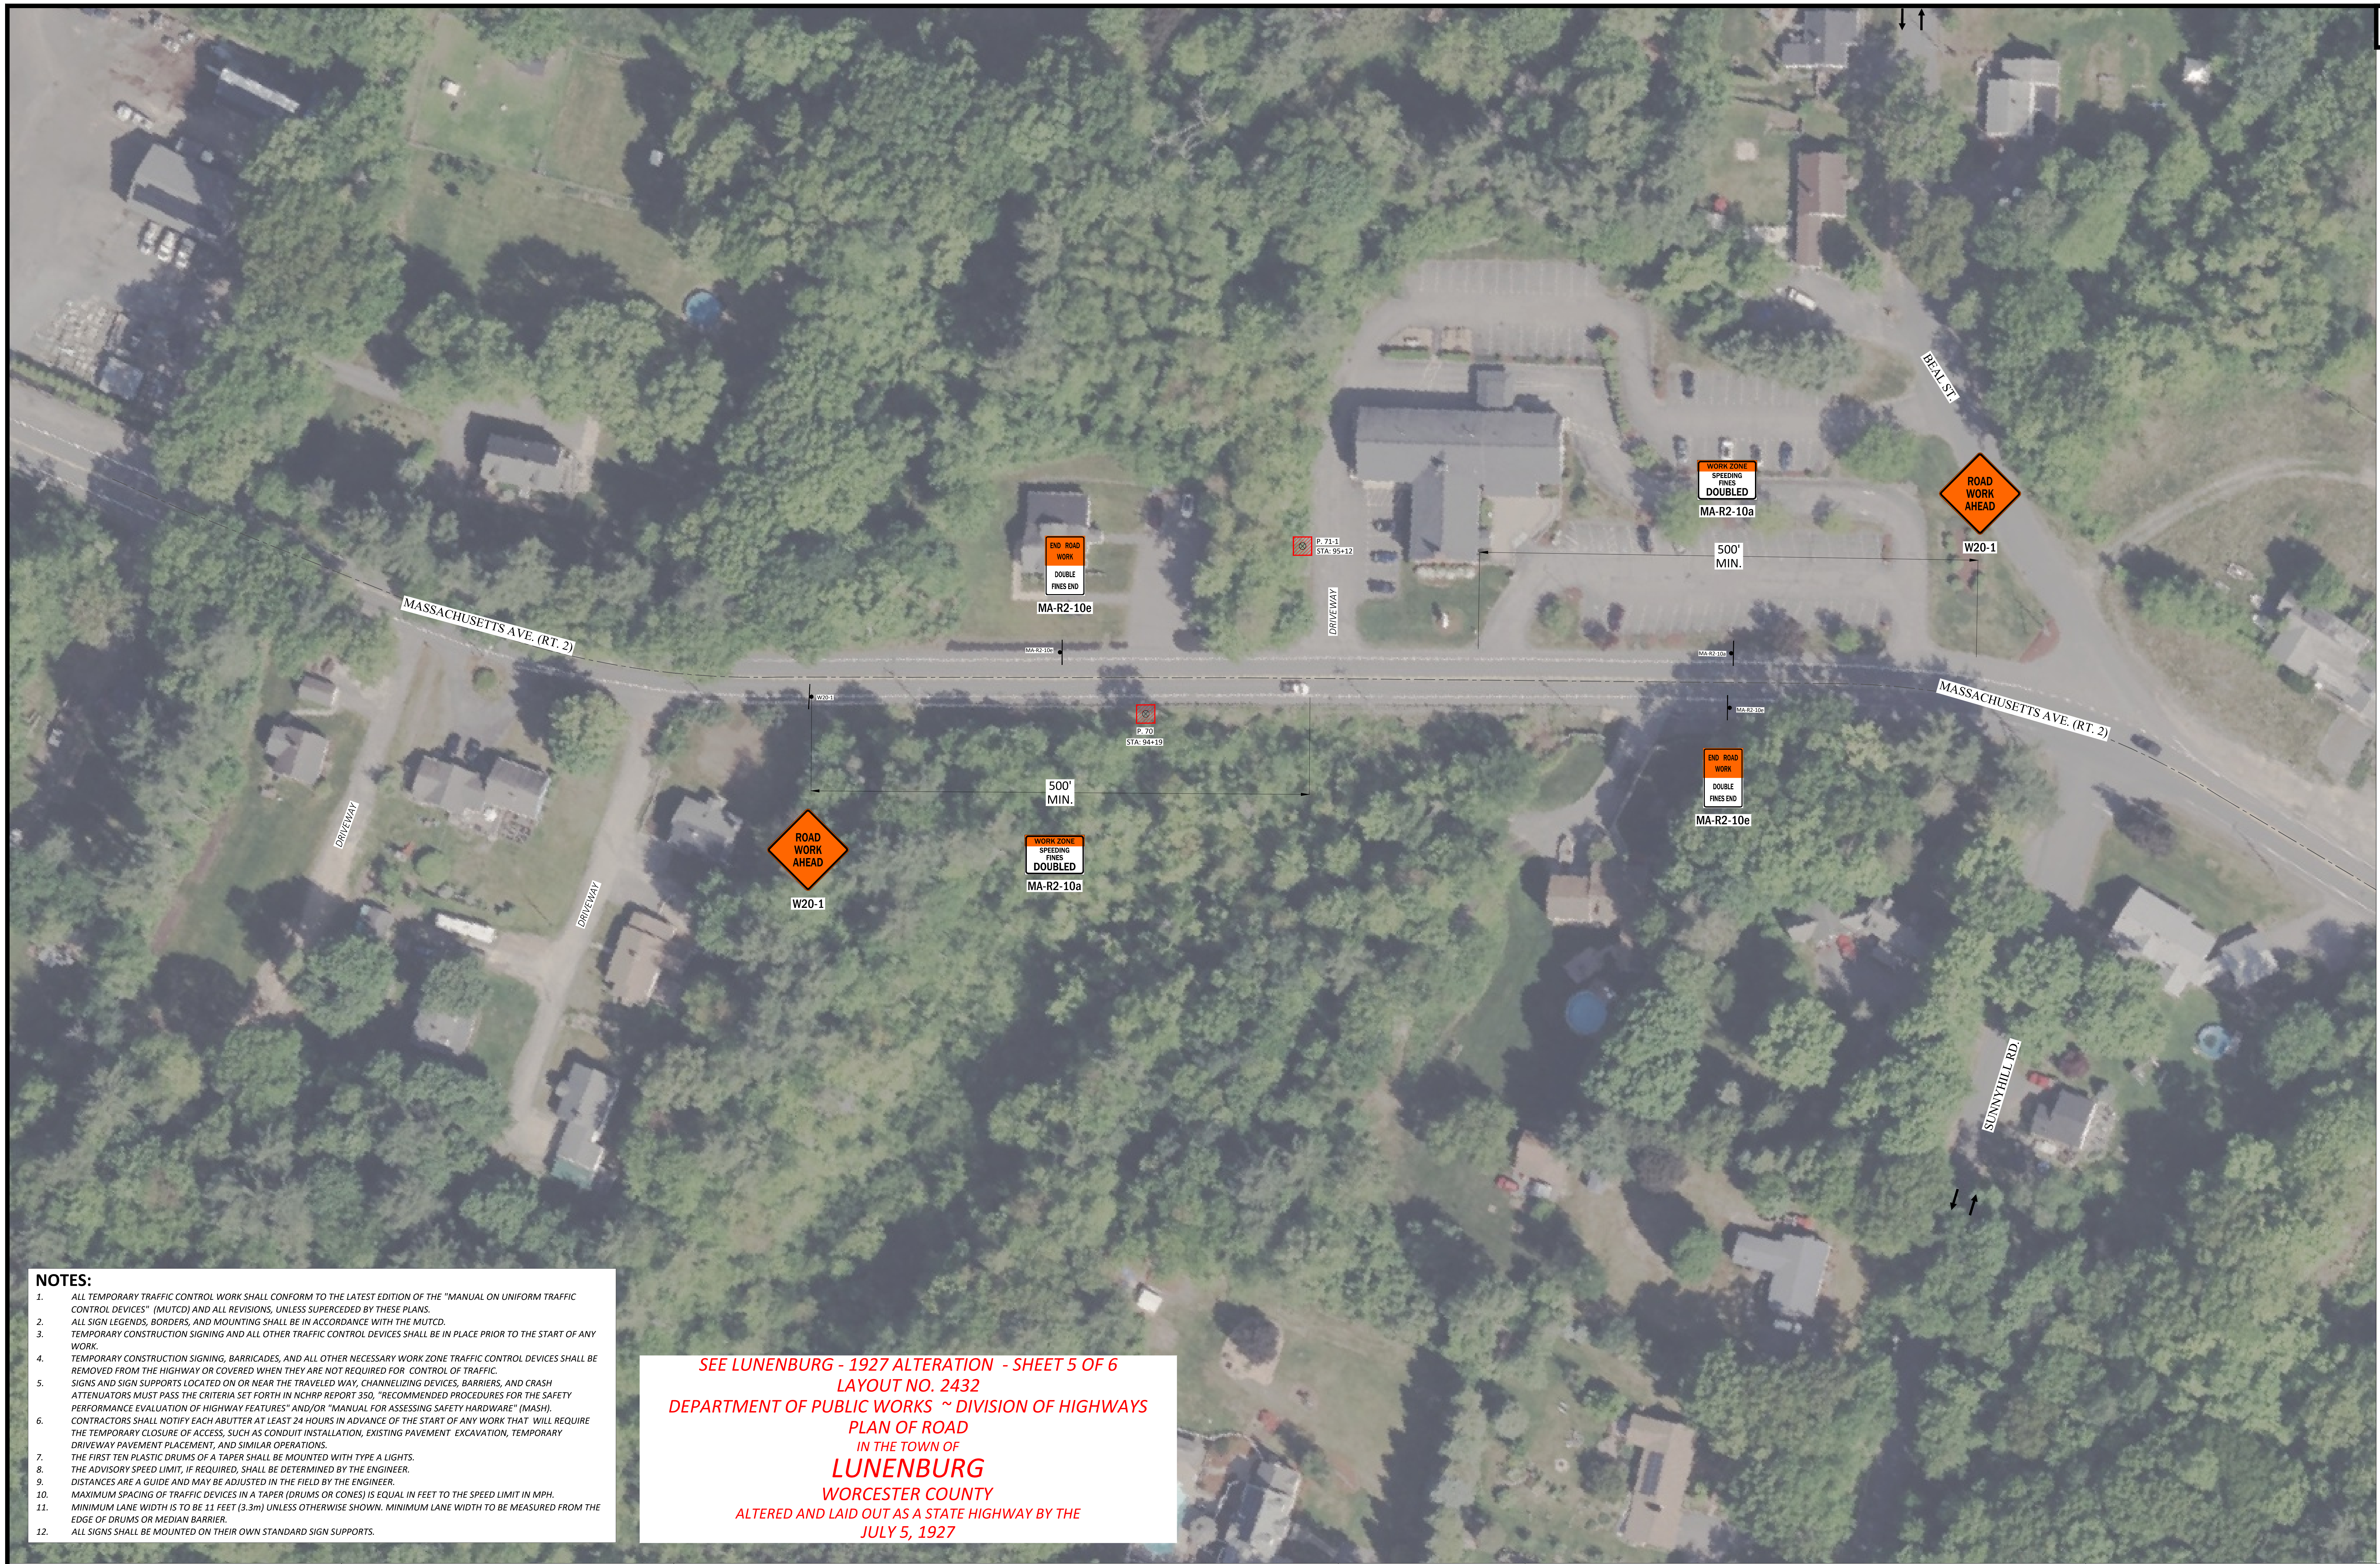

TRAFFIC LEGEND	
▨	WORK ZONE
- - - - - - -	PROPOSED TRENCH
■	CHANNELIZING DEVICE (CONE)
◉	CHANNELIZING DEVICE (BARREL)
⊣	SIGN
	POLICE DETAIL
	SINGLE PARKING METER
	DOUBLE PARKING METER
V	VARIABLE MESSAGE BOARD
●●●	ARROW BOARD
	TYPE 3 BARRICADE
	HIGH LEVEL WARNING DEVICE
	CONSTRUCTION TRUCK
	TRUCK MOUNTED ATTENUATOR
←	1 WAY STREET
⇄	2 WAY STREET
↔	2 WAY TRAFFIC (WORK ZONE)
←	TRAFFIC FLOW (WORK ZONE)
←	TRAFFIC FLOW (WORK ZONE)
←	TRAFFIC FLOW (WORK ZONE)
T	EXISTING MBTA BUS STOP
Ⓣ	RELOCATED MBTA BUS STOP

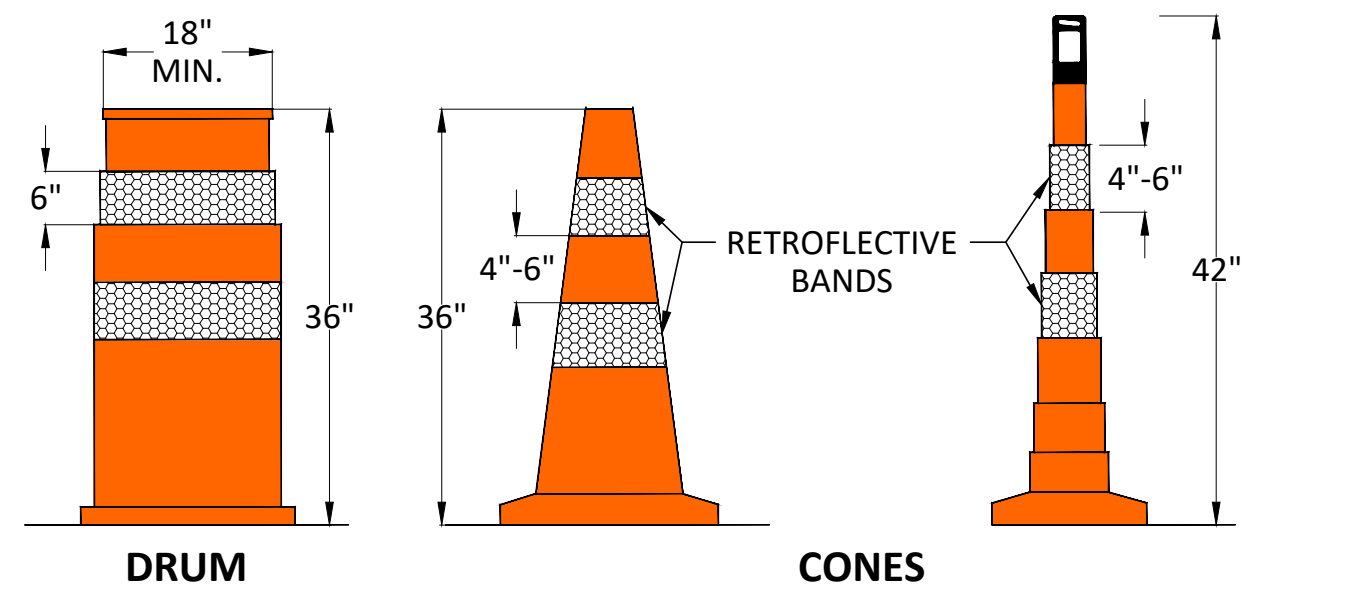

CHANNELIZATION DEVICE DETAIL
TYPICAL
NOT TO SCALE

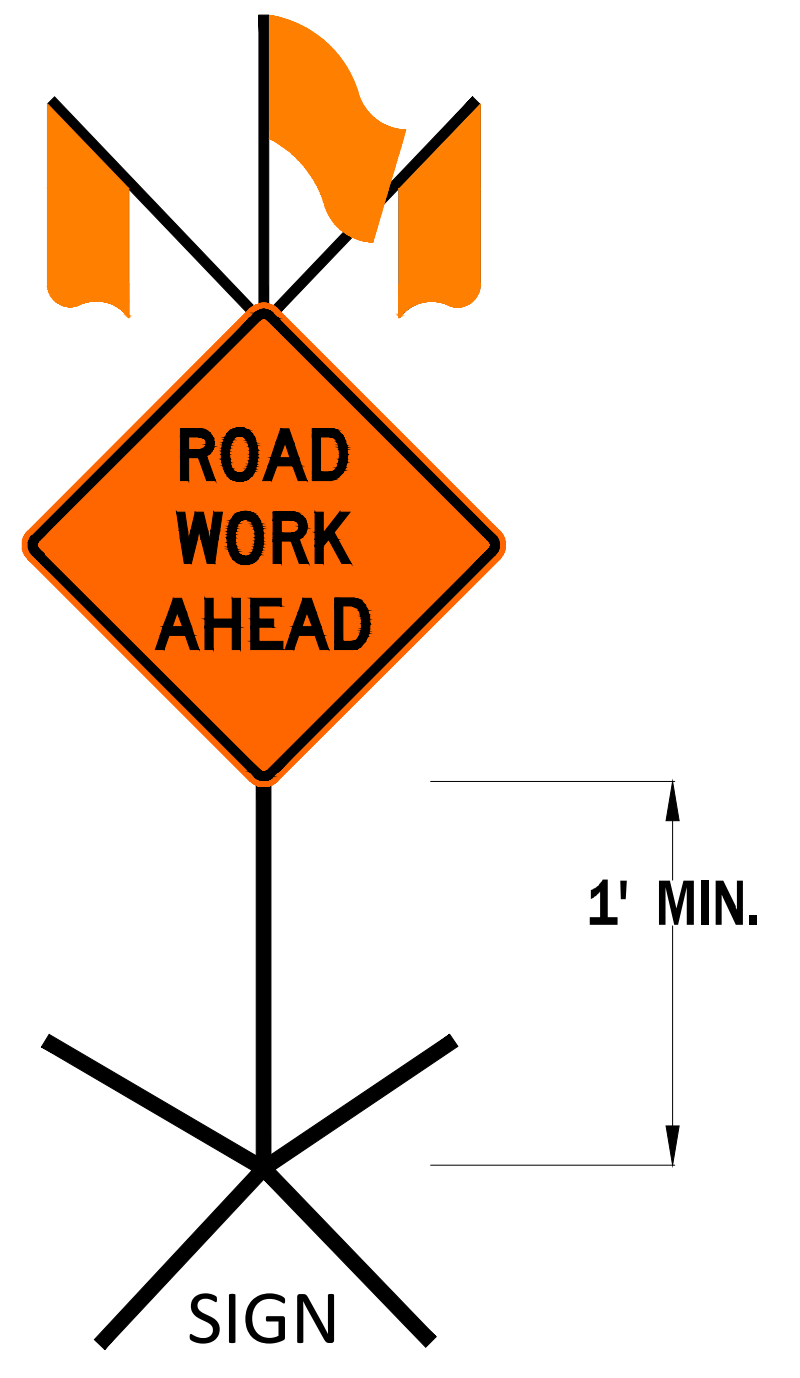

FREE STANDING
SELF SUPPORT SIGN
(TYPICAL)
(NOT TO SCALE)

PAGE 792
PER SEC. 6F.03
MUTCD 11th EDITION
DECEMBER 2023

NOTES:

1. ALL TEMPORARY TRAFFIC CONTROL WORK SHALL CONFORM TO THE LATEST EDITION OF THE "MANUAL ON UNIFORM TRAFFIC CONTROL DEVICES" (MUTCD) AND ALL REVISIONS, UNLESS SUPERCEDED BY THESE PLANS.
2. ALL SIGN LEGENDS, BORDERS, AND MOUNTING SHALL BE IN ACCORDANCE WITH THE MUTCD.
3. TEMPORARY CONSTRUCTION SIGNING AND ALL OTHER TRAFFIC CONTROL DEVICES SHALL BE IN PLACE PRIOR TO THE START OF ANY WORK.
4. TEMPORARY CONSTRUCTION SIGNING, BARRICADES, AND ALL OTHER NECESSARY WORK ZONE TRAFFIC CONTROL DEVICES SHALL BE REMOVED FROM THE HIGHWAY OR COVERED WHEN THEY ARE NOT REQUIRED FOR CONTROL OF TRAFFIC.
5. SIGNS AND SIGN SUPPORTS LOCATED ON OR NEAR THE TRAVELED WAY, CHANNELIZING DEVICES, BARRIERS, AND CRASH ATTENUATORS MUST PASS THE CRITERIA SET FORTH IN NCHRP REPORT 350, "RECOMMENDED PROCEDURES FOR THE SAFETY PERFORMANCE EVALUATION OF HIGHWAY FEATURES" AND/OR "MANUAL FOR ASSESSING SAFETY HARDWARE" (MASH).
6. CONTRACTORS SHALL NOTIFY EACH ABUTTER AT LEAST 24 HOURS IN ADVANCE OF THE START OF ANY WORK THAT WILL REQUIRE THE TEMPORARY CLOSURE OF ACCESS, SUCH AS CONDUIT INSTALLATION, EXISTING PAVEMENT EXCAVATION, TEMPORARY DRIVEWAY PAVEMENT PLACEMENT, AND SIMILAR OPERATIONS.
7. THE FIRST TEN PLASTIC DRUMS OF A TAPER SHALL BE MOUNTED WITH TYPE A LIGHTS.
8. THE ADVISORY SPEED LIMIT, IF REQUIRED, SHALL BE DETERMINED BY THE ENGINEER.
9. DISTANCES ARE A GUIDE AND MAY BE ADJUSTED IN THE FIELD BY THE ENGINEER.
10. MAXIMUM SPACING OF TRAFFIC DEVICES IN A TAPER (DRUMS OR CONES) IS EQUAL IN FEET TO THE SPEED LIMIT IN MPH.
11. MINIMUM LANE WIDTH IS TO BE 11 FEET (3.3m) UNLESS OTHERWISE SHOWN. MINIMUM LANE WIDTH TO BE MEASURED FROM THE EDGE OF DRUMS OR MEDIAN BARRIER.
12. ALL SIGNS SHALL BE MOUNTED ON THEIR OWN STANDARD SIGN SUPPORTS.

SEE LUNENBURG - 1927 ALTERATION - SHEET 5 OF 6
LAYOUT NO. 2432
DEPARTMENT OF PUBLIC WORKS ~ DIVISION OF HIGHWAYS
PLAN OF ROAD
IN THE TOWN OF
LUNENBURG
WORCESTER COUNTY
ALTERED AND LAID OUT AS A STATE HIGHWAY BY THE
JULY 5, 1927

REVISIONS

REV	DESCRIPTION	DATE
--	---	---

NOTE:
EXISTING UTILITIES SHOWN ARE APPROXIMATE AND NOT WARRANTED TO BE CORRECT. THE CONTRACTOR SHALL VERIFY THE LOCATION OF ALL PUBLIC AND PRIVATE UTILITIES PRIOR TO BEGINNING ANY EXCAVATION.

KNOW WHAT'S BELOW
CALL BEFORE YOU DIG
IT'S FREE AND IT'S THE LAW

CALL 811 OR 1-888-DIG-SAFE

NOTES:

- SPEED LIMIT 40 MPH AS NOTED ON THE massDOT ONLINE ROAD INVENTORY.
- POLICE DETAIL TO STOP TRAFFIC FOR NO LONGER THAN 5 MINUTES TO FACILITATE AERIAL CROSSING.
- SIDEWALKS NOT PRESENT ON EITHER SIDE OF MASSACHUSETTS AVE. (ROUTE 2A), ADJACENT TO THE WORK ZONE.
- ALLOW BREAKS IN CHANNELIZATION DEVICES TO PERMIT DRIVEWAY ACCESS.

SCALE:

1"= 30 FEET
0 30 60 90 120

Massachusetts Department of Transportation

PREPARED BY:

PIKE TELECOM
21 Oxford Rd
Mansfield, MA 02048
www.piketelecom.com
1-508-337-7600

PREPARED FOR:

verizon

TITLE:

TRAFFIC MANAGEMENT PLAN - PHASE II
410-603 MASSACHUSETTS AVE. (RT 2A & RT 13)
LUNENBURG, MA 01462

SURVEYED BY: PIKE TELECOM	PRINT NO: 2 OF 3
DRAWN BY: MPO	SCALE: 1" = 50'
DATE: 09/30/26	EWO: 1A8P1SA WPI 3167248

09/30/2026 N:\CADD\VERIZON BAU TMP\2026\AA - TMP\BB - TMP - MA\1A8P1SA WPI 3167248 - 410-603 MASS AVE (RT 2A) - LUNENBURG - massDOT TMP\AA - AUTOCAD\1A8P1SA WPI 3167248 - 410-603 MASS AVE (RT 2A) - LUNENBURG - massDOT TMP.dwg

017850300XXXXXX (- EDIT UCS NUMBER AS NEEDED)

PHASE III

OVERHEAD UTILITY WORK MESSAGE PRIOR TO CONSTRUCTION (DISPLAY 1)	SLOW TRAFFIC AHEAD MESSAGE DURING CONSTRUCTION (DISPLAY 1)
DAYS DATES TIMES MESSAGE PRIOR TO CONSTRUCTION (DISPLAY 2)	BE PREPARED TO STOP MESSAGE DURING CONSTRUCTION (DISPLAY 2)

TYPICAL VARIABLE MESSAGE BOARD
AERIAL CROSSING ADVANCED WARNING TEXT

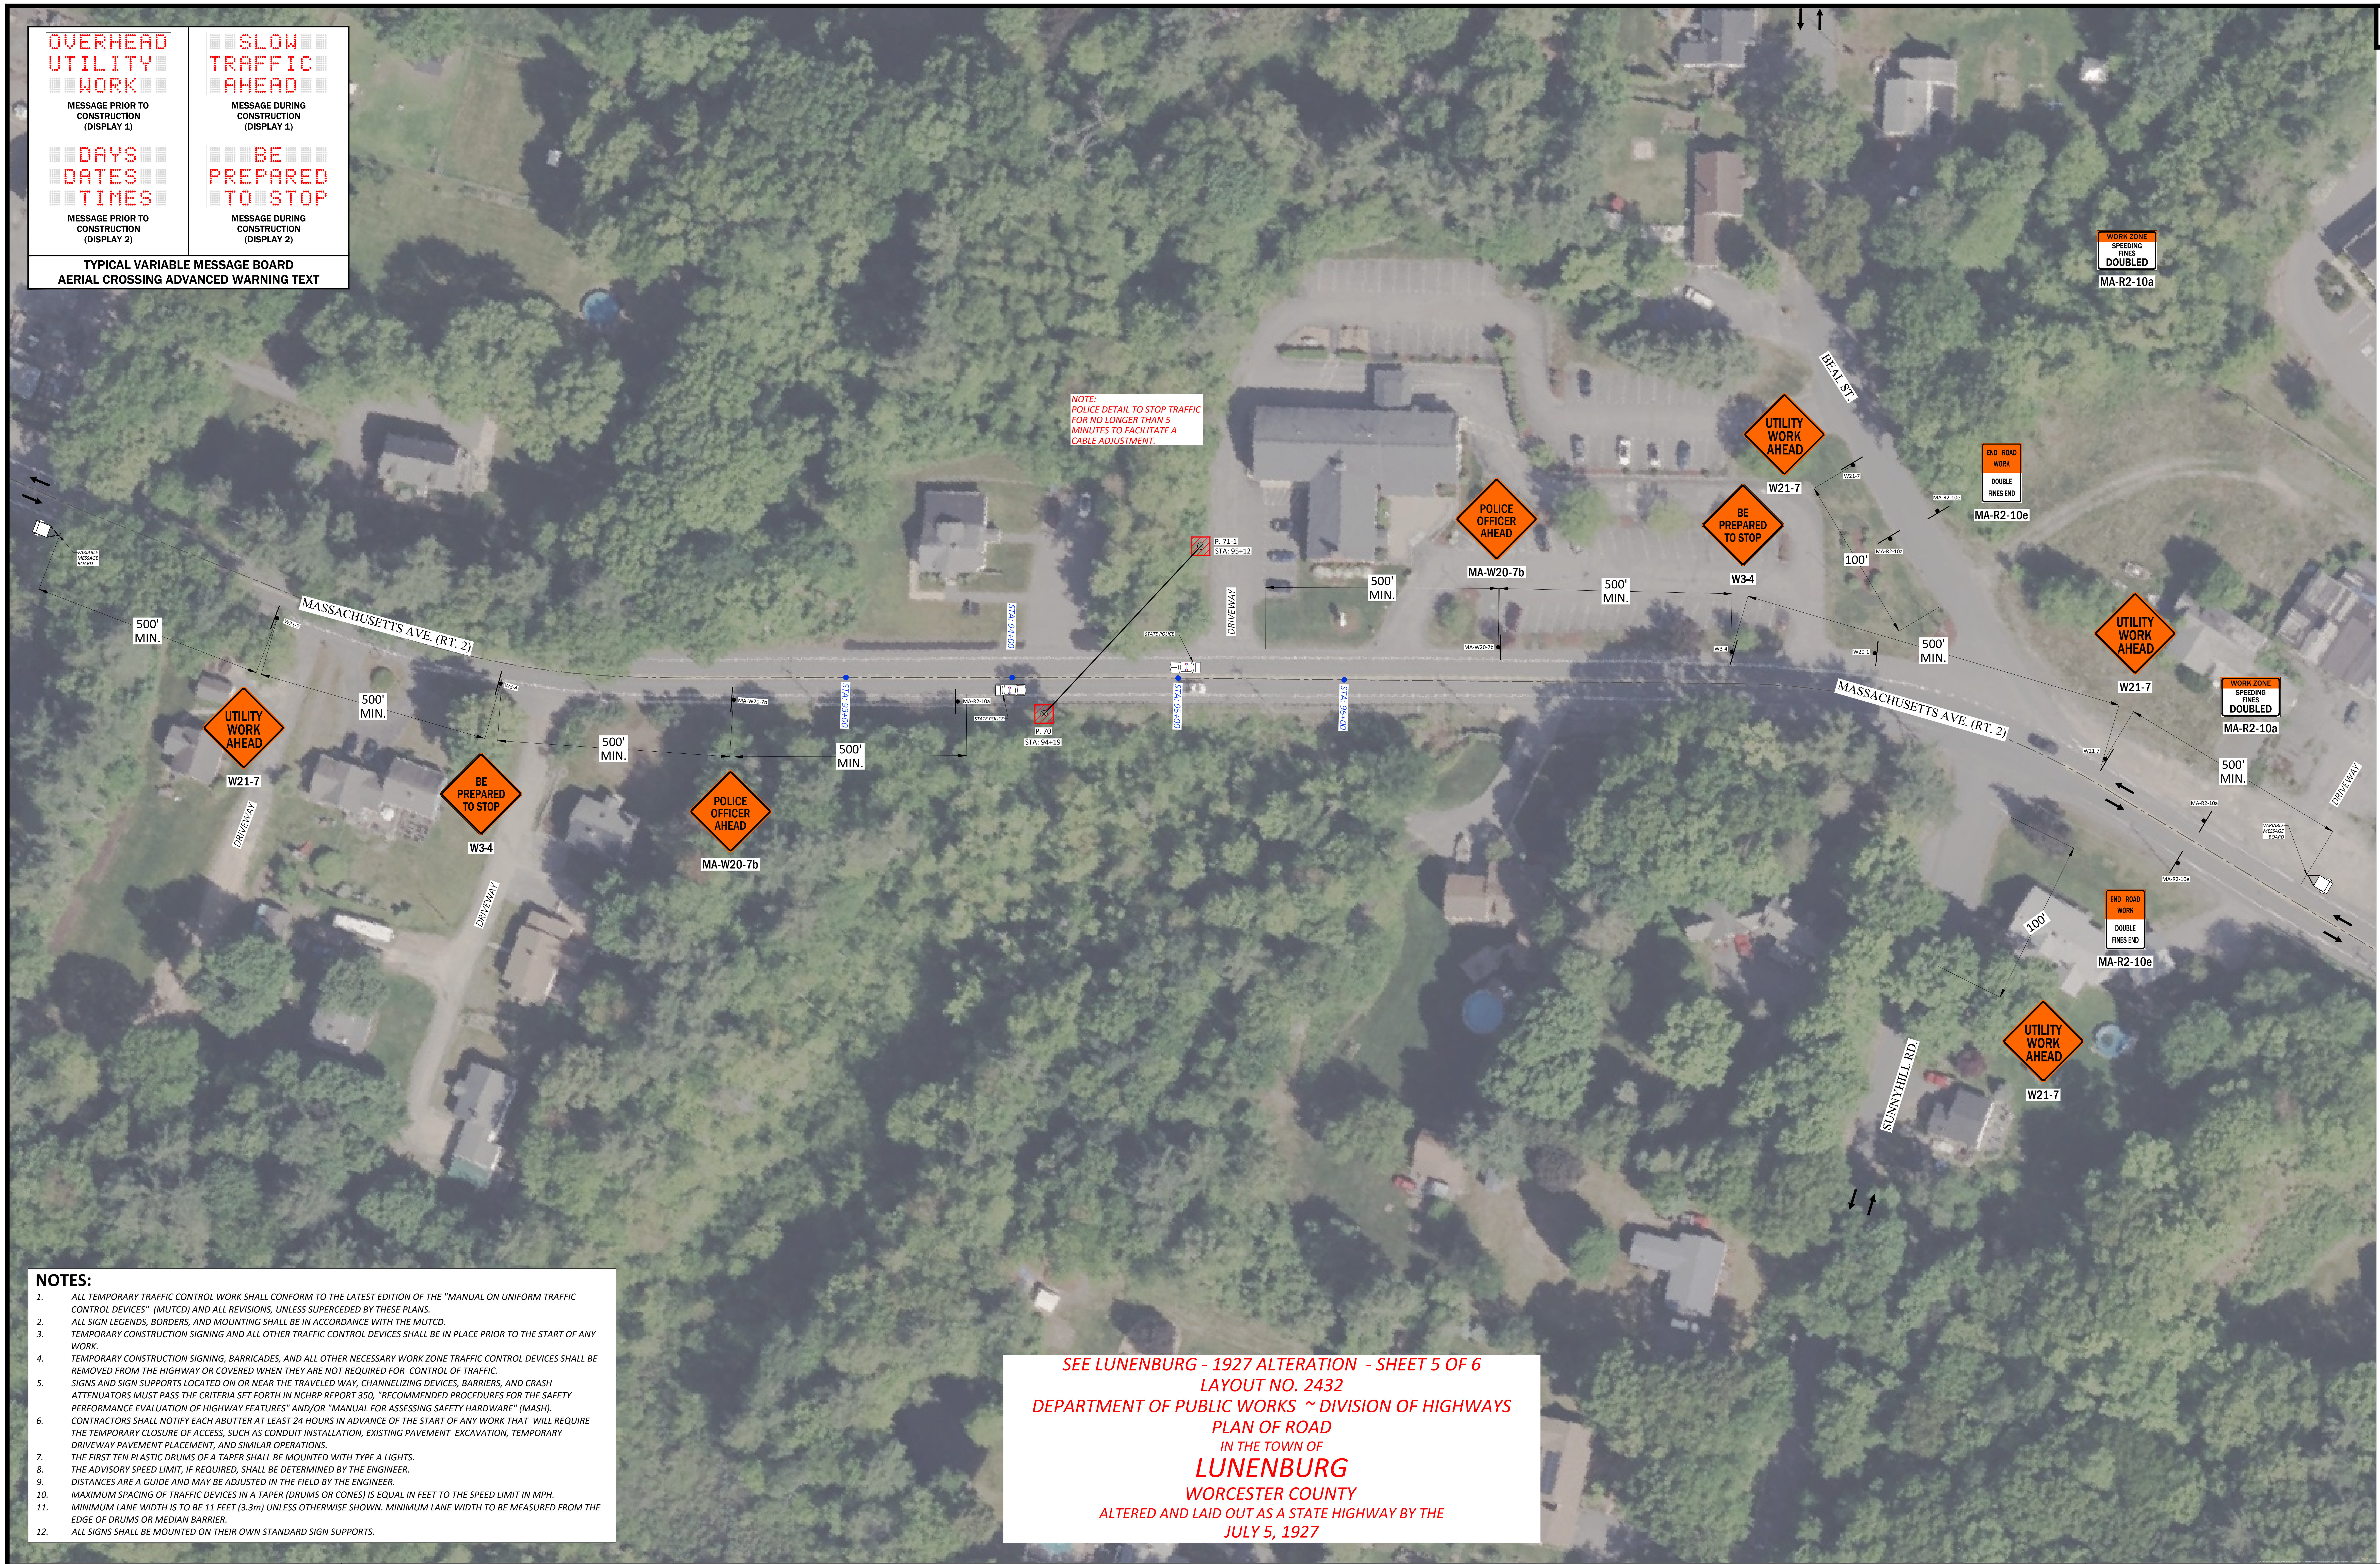

NOTE:
POLICE DETAIL TO STOP TRAFFIC FOR NO LONGER THAN 5 MINUTES TO FACILITATE A CABLE ADJUSTMENT.

NOTES:

1. ALL TEMPORARY TRAFFIC CONTROL WORK SHALL CONFORM TO THE LATEST EDITION OF THE "MANUAL ON UNIFORM TRAFFIC CONTROL DEVICES" (MUTCD) AND ALL REVISIONS, UNLESS SUPERCEDED BY THESE PLANS.
2. ALL SIGN LEGENDS, BORDERS, AND MOUNTING SHALL BE IN ACCORDANCE WITH THE MUTCD.
3. TEMPORARY CONSTRUCTION SIGNING AND ALL OTHER TRAFFIC CONTROL DEVICES SHALL BE IN PLACE PRIOR TO THE START OF ANY WORK.
4. TEMPORARY CONSTRUCTION SIGNING, BARRICADES, AND ALL OTHER NECESSARY WORK ZONE TRAFFIC CONTROL DEVICES SHALL BE REMOVED FROM THE HIGHWAY OR COVERED WHEN THEY ARE NOT REQUIRED FOR CONTROL OF TRAFFIC.
5. SIGNS AND SIGN SUPPORTS LOCATED ON OR NEAR THE TRAVELED WAY, CHANNELIZING DEVICES, BARRIERS, AND CRASH ATTENUATORS MUST PASS THE CRITERIA SET FORTH IN NCHRP REPORT 350, "RECOMMENDED PROCEDURES FOR THE SAFETY PERFORMANCE EVALUATION OF HIGHWAY FEATURES" AND/OR "MANUAL FOR ASSESSING SAFETY HARDWARE" (MASH).
6. CONTRACTORS SHALL NOTIFY EACH ABUTTER AT LEAST 24 HOURS IN ADVANCE OF THE START OF ANY WORK THAT WILL REQUIRE THE TEMPORARY CLOSURE OF ACCESS, SUCH AS CONDUIT INSTALLATION, EXISTING PAVEMENT EXCAVATION, TEMPORARY DRIVEWAY PAVEMENT PLACEMENT, AND SIMILAR OPERATIONS.
7. THE FIRST TEN PLASTIC DRUMS OF A TAPER SHALL BE MOUNTED WITH TYPE A LIGHTS.
8. THE ADVISORY SPEED LIMIT, IF REQUIRED, SHALL BE DETERMINED BY THE ENGINEER.
9. DISTANCES ARE A GUIDE AND MAY BE ADJUSTED IN THE FIELD BY THE ENGINEER.
10. MAXIMUM SPACING OF TRAFFIC DEVICES IN A TAPER (DRUMS OR CONES) IS EQUAL IN FEET TO THE SPEED LIMIT IN MPH.
11. MINIMUM LANE WIDTH IS TO BE 11 FEET (3.3m) UNLESS OTHERWISE SHOWN. MINIMUM LANE WIDTH TO BE MEASURED FROM THE EDGE OF DRUMS OR MEDIAN BARRIER.
12. ALL SIGNS SHALL BE MOUNTED ON THEIR OWN STANDARD SIGN SUPPORTS.

SEE LUNENBURG - 1927 ALTERATION - SHEET 5 OF 6
LAYOUT NO. 2432
DEPARTMENT OF PUBLIC WORKS ~ DIVISION OF HIGHWAYS
PLAN OF ROAD
IN THE TOWN OF
LUNENBURG
WORCESTER COUNTY
ALTERED AND LAID OUT AS A STATE HIGHWAY BY THE
JULY 5, 1927

TRAFFIC LEGEND

▨	WORK ZONE
- - - - - - -	PROPOSED TRENCH
■	CHANNELIZING DEVICE (CONE)
◉	CHANNELIZING DEVICE (BARREL)
┤	SIGN
	POLICE DETAIL
	SINGLE PARKING METER
	DOUBLE PARKING METER
V	VARIABLE MESSAGE BOARD
●●●	ARROW BOARD
▨	TYPE 3 BARRICADE
	HIGH LEVEL WARNING DEVICE
	CONSTRUCTION TRUCK
	TRUCK MOUNTED ATTENUATOR
←	1 WAY STREET
⇄	2 WAY STREET
↔	2 WAY TRAFFIC (WORK ZONE)
←	TRAFFIC FLOW (WORK ZONE)
←	TRAFFIC FLOW (WORK ZONE)
←	TRAFFIC FLOW (WORK ZONE)
Ⓣ	EXISTING MBTA BUS STOP
Ⓣ	RELOCATED MBTA BUS STOP

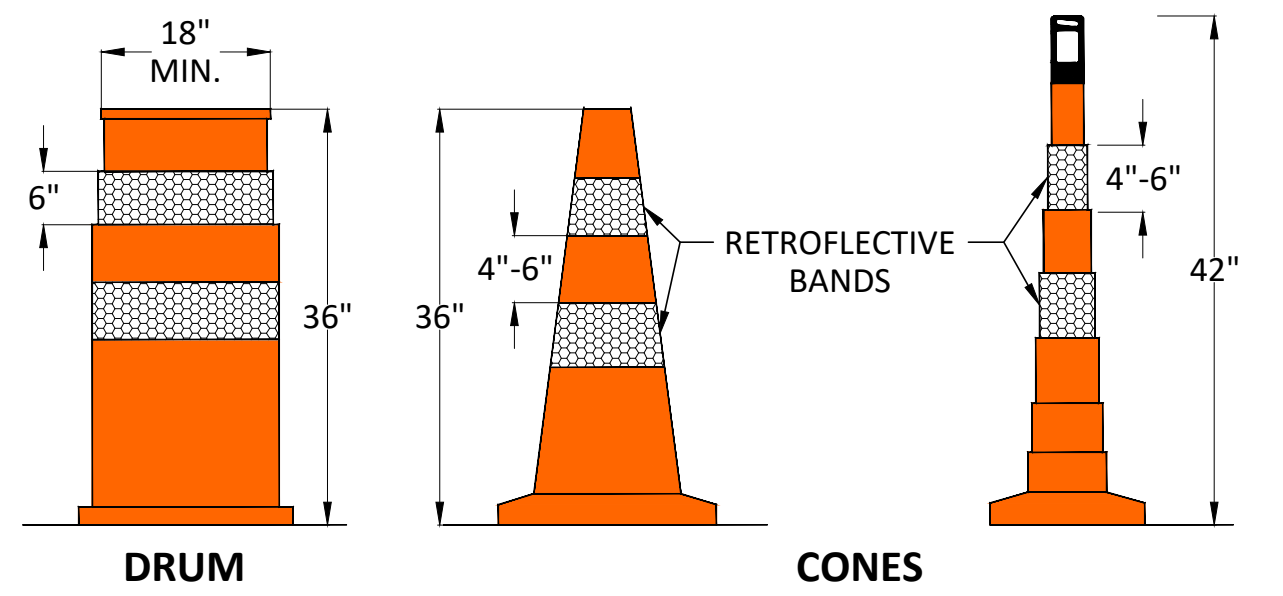

CHANNELIZATION DEVICE DETAIL
TYPICAL
NOT TO SCALE

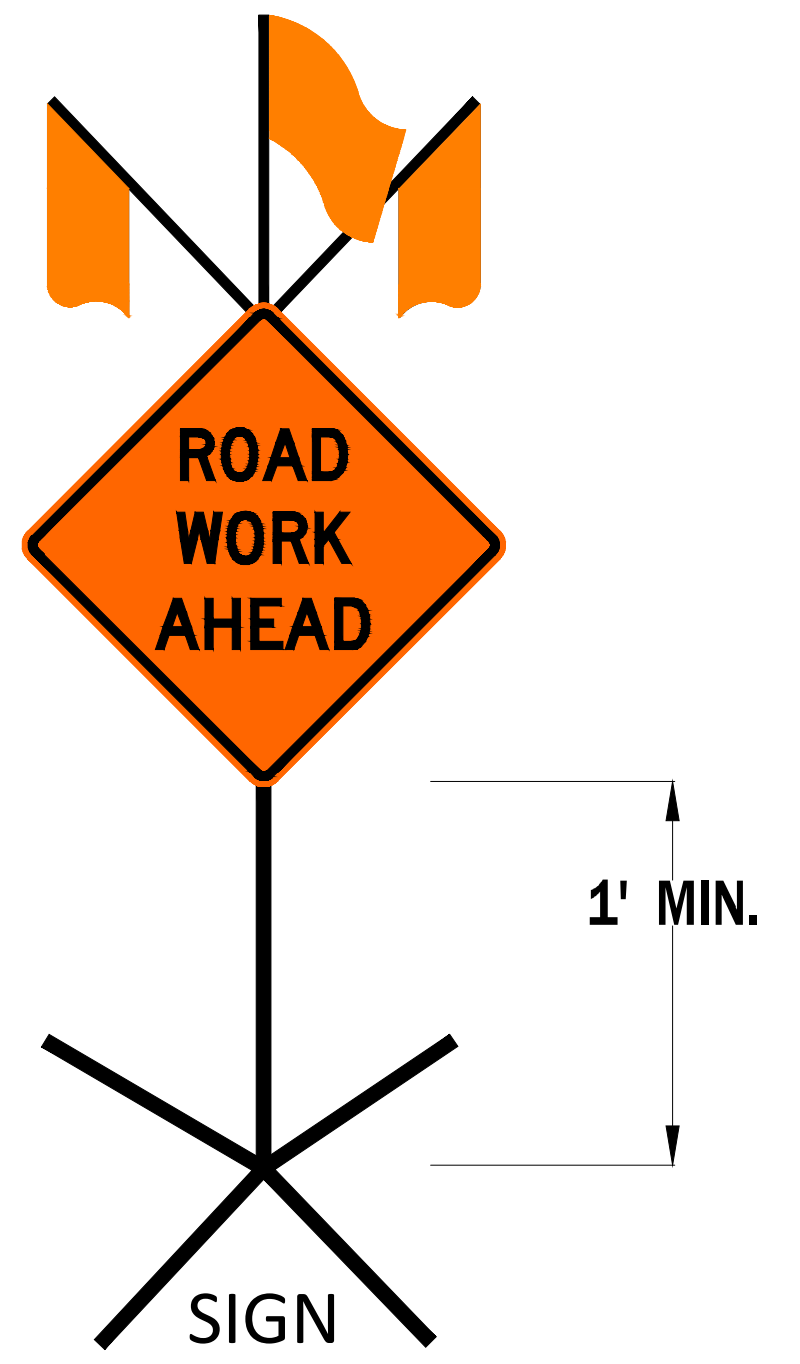

FREE STANDING
SELF SUPPORT SIGN
(TYPICAL)
(NOT TO SCALE)

PAGE 792
PER SEC. 6F.03
MUTCD 11th EDITION
DECEMBER 2023

REVISIONS		
REV	DESCRIPTION	DATE
--	---	---

NOTE:
EXISTING UTILITIES SHOWN ARE APPROXIMATE AND NOT WARRANTED TO BE CORRECT. THE CONTRACTOR SHALL VERIFY THE LOCATION OF ALL PUBLIC AND PRIVATE UTILITIES PRIOR TO BEGINNING ANY EXCAVATION.

NOTES:
- SPEED LIMIT 40 MPH AS NOTED ON THE massDOT ONLINE ROAD INVENTORY.
- POLICE DETAIL TO STOP TRAFFIC FOR NO LONGER THAN 5 MINUTES TO FACILITATE AERIAL CROSSING.
- SIDEWALKS NOT PRESENT ON EITHER SIDE OF MASSACHUSETTS AVE. (ROUTE 2A), ADJACENT TO THE WORK ZONE.
- ALLOW BREAKS IN CHANNELIZATION DEVICES TO PERMIT DRIVEWAY ACCESS.

811 DigSafe MA·ME·NH·RI·VT

KNOW WHAT'S BELOW
CALL BEFORE YOU DIG
IT'S FREE AND IT'S THE LAW
CALL 811 OR 1-888-DIG-SAFE

SCALE:
1"= 60 FEET
0 60 120 180 240

P

massDOT
Massachusetts Department of Transportation

PREPARED BY:
PIKE TELECOM
21 Oxford Rd
Mansfield, MA 02048
www.piketelecom.com
1-508-337-7600

PREPARED FOR:
verizon

TITLE:
TRAFFIC MANAGEMENT PLAN - PHASE III
410-603 MASSACHUSETTS AVE. (RT 2A & RT 13)
LUNENBURG, MA 01462

SURVEYED BY: PIKE TELECOM	PRINT NO: 3 OF 3
DRAWN BY: MPO	SCALE: 1" = 60'
DATE: 09/30/26	EWO: 1A8P1SA WPI 3167248

09/30/2026 N:\CADD\VERIZON BAU TMP\2026\AA - TMP\BB - TMP - MA\1A8P1SA WPI 3167248 - 410-603 MASS AVE (RT 2A) - LUNENBURG - massDOT TMP\AA - AUTOCAD\1A8P1SA WPI 3167248 - 410-603 MASS AVE (RT 2A) - LUNENBURG - massDOT TMP.dwg

017850300XXXXXX (- EDIT UCS NUMBER AS NEEDED)
