PHASE I


NOTES:

1. ALL TEMPORARY TRAFFIC CONTROL WORK SHALL CONFORM TO THE LATEST EDITION OF THE "MANUAL ON UNIFORM TRAFFIC CONTROL DEVICES" (MUTCD) AND ALL REVISIONS, UNLESS SUPERCEDED BY THESE PLANS.
2. ALL SIGN LEGENDS, BORDERS, AND MOUNTING SHALL BE IN ACCORDANCE WITH THE MUTCD.
3. TEMPORARY CONSTRUCTION SIGNING AND ALL OTHER TRAFFIC CONTROL DEVICES SHALL BE IN PLACE PRIOR TO THE START OF ANY WORK.
4. TEMPORARY CONSTRUCTION SIGNING, BARRICADES, AND ALL OTHER NECESSARY WORK ZONE TRAFFIC CONTROL DEVICES SHALL BE REMOVED FROM THE HIGHWAY OR COVERED WHEN THEY ARE NOT REQUIRED FOR CONTROL OF TRAFFIC.
5. SIGNS AND SIGN SUPPORTS LOCATED ON OR NEAR THE TRAVELED WAY, CHANNELIZING DEVICES, BARRIERS, AND CRASH ATTENUATORS MUST PASS THE CRITERIA SET FORTH IN NCHRP REPORT 350, "RECOMMENDED PROCEDURES FOR THE SAFETY PERFORMANCE EVALUATION OF HIGHWAY FEATURES" AND/OR "MANUAL FOR ASSESSING SAFETY HARDWARE" (MASH).
6. CONTRACTORS SHALL NOTIFY EACH ABUTTER AT LEAST 24 HOURS IN ADVANCE OF THE START OF ANY WORK THAT WILL REQUIRE THE TEMPORARY CLOSURE OF ACCESS, SUCH AS CONDUIT INSTALLATION, EXISTING PAVEMENT EXCAVATION, TEMPORARY DRIVEWAY PAVEMENT PLACEMENT, AND SIMILAR OPERATIONS.
7. THE FIRST TEN PLASTIC DRUMS OF A TAPER SHALL BE MOUNTED WITH TYPE A LIGHTS.
8. THE ADVISORY SPEED LIMIT, IF REQUIRED, SHALL BE DETERMINED BY THE ENGINEER.
9. DISTANCES ARE A GUIDE AND MAY BE ADJUSTED IN THE FIELD BY THE ENGINEER.
10. MAXIMUM SPACING OF TRAFFIC DEVICES IN A TAPER (DRUMS OR CONES) IS EQUAL IN FEET TO THE SPEED LIMIT IN MPH.
11. MINIMUM LANE WIDTH IS TO BE 11 FEET (3.3m) UNLESS OTHERWISE SHOWN. MINIMUM LANE WIDTH TO BE MEASURED FROM THE EDGE OF DRUMS OR MEDIAN BARRIER.
12. ALL SIGNS SHALL BE MOUNTED ON THEIR OWN STANDARD SIGN SUPPORTS.




TRAFFIC LEGEND

	WORK ZONE
	PROPOSED TRENCH
	CHANNELIZING DEVICE (CONE)
	CHANNELIZING DEVICE (BARREL)
	SIGN
	POLICE DETAIL
	SINGLE PARKING METER
	DOUBLE PARKING METER
V	VARIABLE MESSAGE BOARD
	ARROW BOARD
	TYPE 3 BARRICADE
	HIGH LEVEL WARNING DEVICE
	CONSTRUCTION TRUCK
	TRUCK MOUNTED ATTENUATOR
	1 WAY STREET
	2 WAY STREET
	2 WAY TRAFFIC (WORK ZONE)
	TRAFFIC FLOW (WORK ZONE)
	TRAFFIC FLOW (WORK ZONE)
	TRAFFIC FLOW (WORK ZONE)
T	EXISTING MBTA BUS STOP
T	RELOCATED MBTA BUS STOP



CHANNELIZATION DEVICE DETAIL
TYPICAL
NOT TO SCALE



FREE STANDING
SELF SUPPORT SIGN
(TYPICAL)
(NOT TO SCALE)

PAGE 792
PER SEC. 6F.03
MUTCD 11th EDITION
DECEMBER 2023

REVISIONS		
REV	DESCRIPTION	DATE
--	---	---

NOTE:
EXISTING UTILITIES SHOWN ARE APPROXIMATE AND NOT WARRANTED TO BE CORRECT. THE CONTRACTOR SHALL VERIFY THE LOCATION OF ALL PUBLIC AND PRIVATE UTILITIES PRIOR TO BEGINNING ANY EXCAVATION.

811 DigSafe
KNOW WHAT'S BELOW
CALL BEFORE YOU DIG
IT'S FREE AND IT'S THE LAW
CALL 811 OR 1-888-DIG-SAFE

NOTES:
- SPEED LIMIT IN THE CITY OF BOSTON IS 25 MPH.
- ALLOW BREAKS IN CHANNELIZATION DEVICES TO PERMIT DRIVEWAY ACCESS.

SCALE:
1"= 40 FEET
0 40 80 120 160

PREPARED BY:
PIKE TELECOM
21 Oxford Rd
Mansfield, MA 02048
www.piketelecom.com
1-508-337-7600

PREPARED FOR:
verizon

TITLE:
TRAFFIC MANAGEMENT PLAN - PHASE I
E SECOND ST
BOSTON, MA 02127


SURVEYED BY: PIKE TELECOM	PRINT NO: 1 OF 2
DRAWN BY: MM	SCALE: 1" = 40'
DATE: 10/13/26	EWO: 1A8J1KB WPI 3171586

10/13/2026 Y:\PIKE\TMP\non-mass\DOT - MA\1A8J1KB WPI 3171586, E Second St, South Boston, MA\1A8J1KB WPI 3171586, E Second St, South Boston, MA - TMP.dwg

PHASE II

NOTES:

1. ALL TEMPORARY TRAFFIC CONTROL WORK SHALL CONFORM TO THE LATEST EDITION OF THE "MANUAL ON UNIFORM TRAFFIC CONTROL DEVICES" (MUTCD) AND ALL REVISIONS, UNLESS SUPERCEDED BY THESE PLANS.
2. ALL SIGN LEGENDS, BORDERS, AND MOUNTING SHALL BE IN ACCORDANCE WITH THE MUTCD.
3. TEMPORARY CONSTRUCTION SIGNING AND ALL OTHER TRAFFIC CONTROL DEVICES SHALL BE IN PLACE PRIOR TO THE START OF ANY WORK.
4. TEMPORARY CONSTRUCTION SIGNING, BARRICADES, AND ALL OTHER NECESSARY WORK ZONE TRAFFIC CONTROL DEVICES SHALL BE REMOVED FROM THE HIGHWAY OR COVERED WHEN THEY ARE NOT REQUIRED FOR CONTROL OF TRAFFIC.
5. SIGNS AND SIGN SUPPORTS LOCATED ON OR NEAR THE TRAVELED WAY, CHANNELIZING DEVICES, BARRIERS, AND CRASH ATTENUATORS MUST PASS THE CRITERIA SET FORTH IN NCHRP REPORT 350, "RECOMMENDED PROCEDURES FOR THE SAFETY PERFORMANCE EVALUATION OF HIGHWAY FEATURES" AND/OR "MANUAL FOR ASSESSING SAFETY HARDWARE" (MASH).
6. CONTRACTORS SHALL NOTIFY EACH ABUTTER AT LEAST 24 HOURS IN ADVANCE OF THE START OF ANY WORK THAT WILL REQUIRE THE TEMPORARY CLOSURE OF ACCESS, SUCH AS CONDUIT INSTALLATION, EXISTING PAVEMENT EXCAVATION, TEMPORARY DRIVEWAY PAVEMENT PLACEMENT, AND SIMILAR OPERATIONS.
7. THE FIRST TEN PLASTIC DRUMS OF A TAPER SHALL BE MOUNTED WITH TYPE A LIGHTS.
8. THE ADVISORY SPEED LIMIT, IF REQUIRED, SHALL BE DETERMINED BY THE ENGINEER.
9. DISTANCES ARE A GUIDE AND MAY BE ADJUSTED IN THE FIELD BY THE ENGINEER.
10. MAXIMUM SPACING OF TRAFFIC DEVICES IN A TAPER (DRUMS OR CONES) IS EQUAL IN FEET TO THE SPEED LIMIT IN MPH.
11. MINIMUM LANE WIDTH IS TO BE 11 FEET (3.3m) UNLESS OTHERWISE SHOWN. MINIMUM LANE WIDTH TO BE MEASURED FROM THE EDGE OF DRUMS OR MEDIAN BARRIER.
12. ALL SIGNS SHALL BE MOUNTED ON THEIR OWN STANDARD SIGN SUPPORTS.

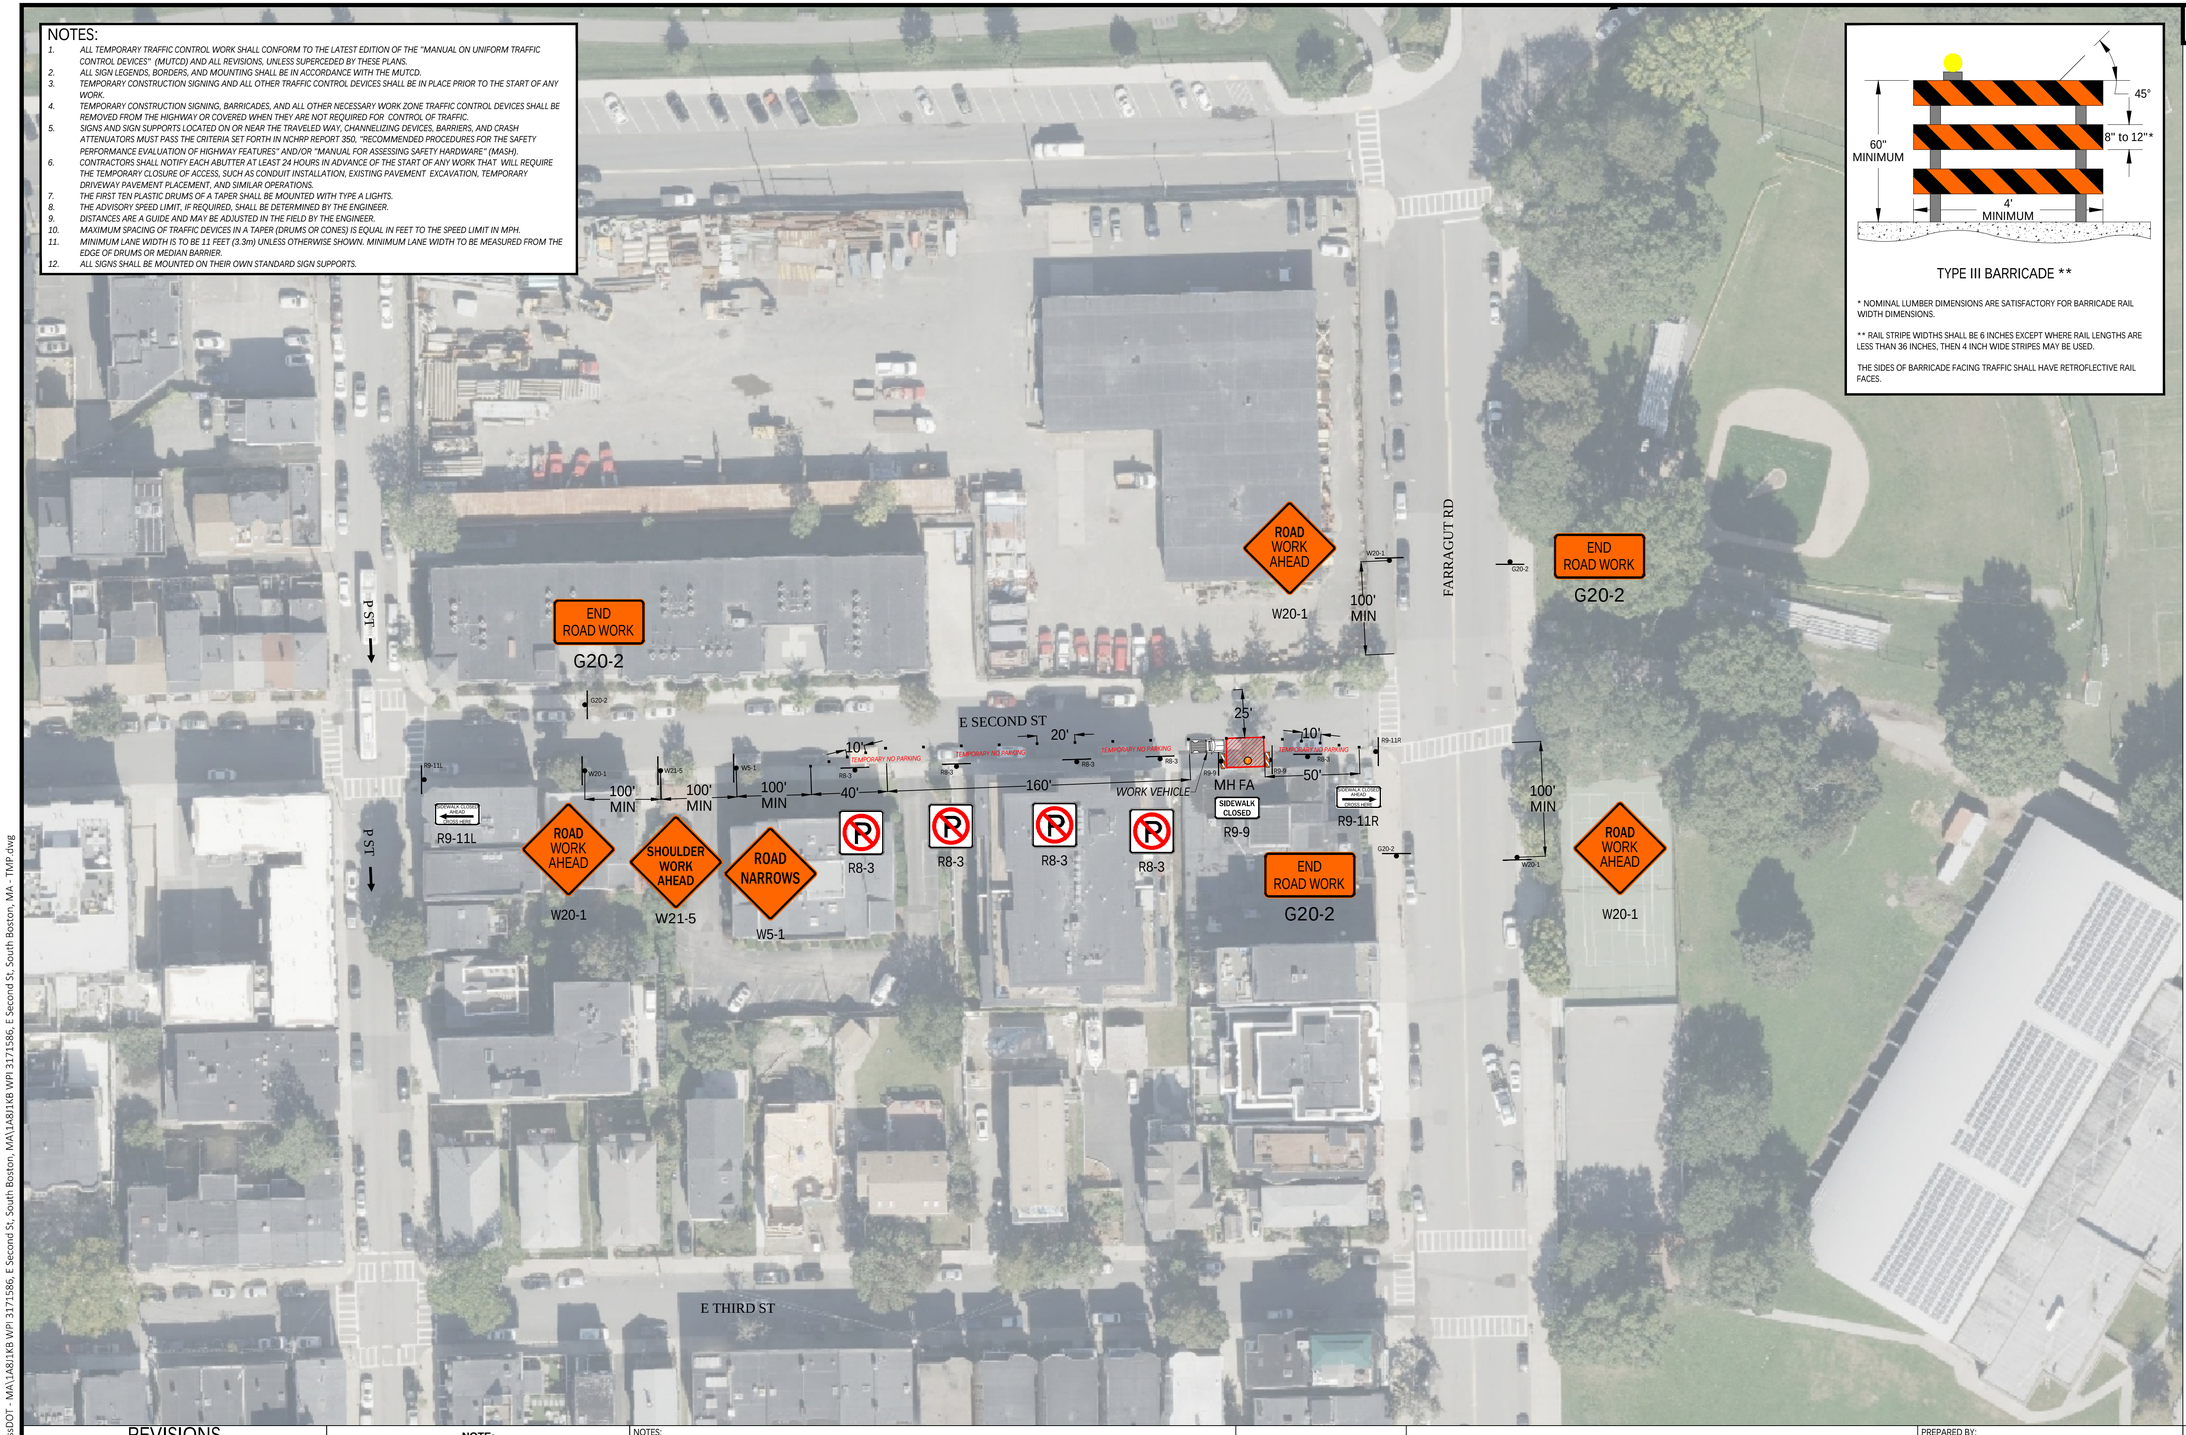

TYPE III BARRICADE **


* NOMINAL LUMBER DIMENSIONS ARE SATISFACTORY FOR BARRICADE RAIL WIDTH DIMENSIONS.

** RAIL STRIPE WIDTHS SHALL BE 6 INCHES EXCEPT WHERE RAIL LENGTHS ARE LESS THAN 36 INCHES, THEN 4 INCH WIDE STRIPES MAY BE USED.


THE SIDES OF BARRICADE FACING TRAFFIC SHALL HAVE RETROFLECTIVE RAIL FACES.

TRAFFIC LEGEND

	WORK ZONE
	PROPOSED TRENCH
■	CHANNELIZING DEVICE (CONE)
◉	CHANNELIZING DEVICE (BARREL)
	SIGN
	POLICE DETAIL
	SINGLE PARKING METER
	DOUBLE PARKING METER
V	VARIABLE MESSAGE BOARD
	ARROW BOARD
	TYPE 3 BARRICADE
	HIGH LEVEL WARNING DEVICE
	CONSTRUCTION TRUCK
	TRUCK MOUNTED ATTENUATOR
	1 WAY STREET
	2 WAY STREET
	2 WAY TRAFFIC (WORK ZONE)
	TRAFFIC FLOW (WORK ZONE)
	TRAFFIC FLOW (WORK ZONE)
	TRAFFIC FLOW (WORK ZONE)
Ⓣ	EXISTING MBTA BUS STOP
Ⓣ	RELOCATED MBTA BUS STOP



CHANNELIZATION DEVICE DETAIL
TYPICAL
NOT TO SCALE



FREE STANDING
SELF SUPPORT SIGN
(TYPICAL)
(NOT TO SCALE)

PAGE 792
PER SEC. 6F.03
MUTCD 11th EDITION
DECEMBER 2023

REVISIONS

REV	DESCRIPTION	DATE
--	---	---

NOTE:
EXISTING UTILITIES SHOWN ARE APPROXIMATE AND NOT WARRANTED TO BE CORRECT. THE CONTRACTOR SHALL VERIFY THE LOCATION OF ALL PUBLIC AND PRIVATE UTILITIES PRIOR TO BEGINNING ANY EXCAVATION.

811 DigSafe
KNOW WHAT'S BELOW
CALL BEFORE YOU DIG
IT'S FREE AND IT'S THE LAW
CALL 811 OR 1-888-DIG-SAFE

NOTES:
- SPEED LIMIT IN THE CITY OF BOSTON IS 25 MPH.
- ALLOW BREAKS IN CHANNELIZATION DEVICES TO PERMIT DRIVEWAY ACCESS.

SCALE: 1"= 40 FEET
0 40 80 120 160

PREPARED BY:
PIKE TELECOM
21 Oxford Rd
Mansfield, MA 02048
www.piketelecom.com
1-508-337-7600

PREPARED FOR:
verizon

TITLE:
TRAFFIC MANAGEMENT PLAN - PHASE II
E SECOND ST
BOSTON, MA 02127

SURVEYED BY: PIKE TELECOM	PRINT NO: 2 OF 2
DRAWN BY: MM	SCALE: 1" = 40'
DATE: 10/13/26	EWO: 1A8J1KB WPI 3171586

10/13/2026 Y:\PIKE\TMP\non-massDOT - MA\1A8J1KB WPI 3171586, E Second St, South Boston, MA\1A8J1KB WPI 3171586, E Second St, South Boston, MA - TMP.dwg
