
PHASE I



NOTES:

1. *ALL TEMPORARY TRAFFIC CONTROL WORK SHALL CONFORM TO THE LATEST EDITION OF THE "MANUAL ON UNIFORM TRAFFIC CONTROL DEVICES" (MUTCD) AND ALL REVISIONS, UNLESS SUPERCEDED BY THESE PLANS.*
2. *ALL SIGN LEGENDS, BORDERS, AND MOUNTING SHALL BE IN ACCORDANCE WITH THE MUTCD.*
3. *TEMPORARY CONSTRUCTION SIGNING AND ALL OTHER TRAFFIC CONTROL DEVICES SHALL BE IN PLACE PRIOR TO THE START OF ANY WORK.*
4. *TEMPORARY CONSTRUCTION SIGNING, BARRICADES, AND ALL OTHER NECESSARY WORK ZONE TRAFFIC CONTROL DEVICES SHALL BE REMOVED FROM THE HIGHWAY OR COVERED WHEN THEY ARE NOT REQUIRED FOR CONTROL OF TRAFFIC.*
5. *SIGNS AND SIGN SUPPORTS LOCATED ON OR NEAR THE TRAVELED WAY, CHANNELIZING DEVICES, BARRIERS, AND CRASH ATTENUATORS MUST PASS THE CRITERIA SET FORTH IN NCHRP REPORT 350, "RECOMMENDED PROCEDURES FOR THE SAFETY PERFORMANCE EVALUATION OF HIGHWAY FEATURES" AND/OR "MANUAL FOR ASSESSING SAFETY HARDWARE" (MASH).*
6. *CONTRACTORS SHALL NOTIFY EACH ABUTTER AT LEAST 24 HOURS IN ADVANCE OF THE START OF ANY WORK THAT WILL REQUIRE THE TEMPORARY CLOSURE OF ACCESS, SUCH AS CONDUIT INSTALLATION, EXISTING PAVEMENT EXCAVATION, TEMPORARY DRIVEWAY PAVEMENT PLACEMENT, AND SIMILAR OPERATIONS.*
7. *THE FIRST TEN PLASTIC DRUMS OF A TAPER SHALL BE MOUNTED WITH TYPE A LIGHTS.*
8. *THE ADVISORY SPEED LIMIT, IF REQUIRED, SHALL BE DETERMINED BY THE ENGINEER.*
9. *DISTANCES ARE A GUIDE AND MAY BE ADJUSTED IN THE FIELD BY THE ENGINEER.*
10. *MAXIMUM SPACING OF TRAFFIC DEVICES IN A TAPER (DRUMS OR CONES) IS EQUAL IN FEET TO THE SPEED LIMIT IN MPH.*
11. *MINIMUM LANE WIDTH IS TO BE 11 FEET (3.3m) UNLESS OTHERWISE SHOWN. MINIMUM LANE WIDTH TO BE MEASURED FROM THE EDGE OF DRUMS OR MEDIAN BARRIER.*
12. *ALL SIGNS SHALL BE MOUNTED ON THEIR OWN STANDARD SIGN SUPPORTS.*

TRAFFIC LEGEND	
	WORK ZONE
	PROPOSED TRENCH
■	CHANNELIZING DEVICE (CONE)
◉	CHANNELIZING DEVICE (BARREL)
	SIGN
	POLICE DETAIL
	SINGLE PARKING METER
	DOUBLE PARKING METER
V	VARIABLE MESSAGE BOARD
	ARROW BOARD
	TYPE 3 BARRICADE
	HIGH LEVEL WARNING DEVICE
	CONSTRUCTION TRUCK
	TRUCK MOUNTED ATTENUATOR
	1 WAY STREET
	2 WAY STREET
	2 WAY TRAFFIC (WORK ZONE)
	TRAFFIC FLOW (WORK ZONE)
	TRAFFIC FLOW (WORK ZONE)
	TRAFFIC FLOW (WORK ZONE)
Ⓡ	EXISTING RIPTA BUS STOP
Ⓡ	RELOCATED RIPTA BUS STOP




CHANNELIZATION DEVICE DETAIL
TYPICAL
NOT TO SCALE

TYPE III BARRICADE **

* NOMINAL LUMBER DIMENSIONS ARE SATISFACTORY FOR BARRICADE RAIL WIDTH DIMENSIONS.

** RAIL STRIPE WIDTHS SHALL BE 6 INCHES EXCEPT WHERE RAIL LENGTHS ARE LESS THAN 36 INCHES, THEN 4 INCH WIDE STRIPES MAY BE USED.

THE SIDES OF BARRICADE FACING TRAFFIC SHALL HAVE RETROFLECTIVE RAIL FACES.



FREE STANDING
SELF SUPPORT SIGN
(TYPICAL)
(NOT TO SCALE)

PAGE 792
PER SEC. 6F.03
MUTCD 11th EDITION
DECEMBER 2023

REVISIONS

REV	DESCRIPTION	DATE
--	---	---

NOTE:
EXISTING UTILITIES SHOWN ARE APPROXIMATE AND NOT WARRANTED TO BE CORRECT. THE CONTRACTOR SHALL VERIFY THE LOCATION OF ALL PUBLIC AND PRIVATE UTILITIES PRIOR TO BEGINNING ANY EXCAVATION.

811 DigSafe MA ME NH RI VT

KNOW WHAT'S BELOW
CALL BEFORE YOU DIG
IT'S FREE AND IT'S THE LAW

CALL 811 OR 1-888-DIG-SAFE

NOTES:
- SPEED LIMIT 25 MPH AS OBSERVED IN THE FIELD.
- ALLOW BREAKS IN CHANNELIZATION DEVICES TO PERMIT DRIVEWAY ACCESS.

SCALE:

1"= 40 FEET

0 40 80 120 160

PREPARED BY:

PIKE TELECOM
21 Oxford Rd
Mansfield, MA 02048
www.piketelecom.com
1-508-337-7600

PREPARED FOR:

verizon

TITLE:


TRAFFIC MANAGEMENT PLAN - PHASE I
GRANITE ST (US-1)
WESTERLY, RI 02891

SURVEYED BY: PIKE TELECOM	PRINT NO: 1 OF 6
DRAWN BY: SHB	SCALE: 1" = 40'
DATE: 10/15/26	EWO: 1A8L6XS WPI 3178233

10/20/2026 N:\CADD\VERIZON BAU TMP\2026\AA - TMP\RI\1A8L6XS WPI 3178233 - 125-165 GRANITE ST (US-1), WESTERLY, RI - TMP.dwg

018150300411645

PHASE II

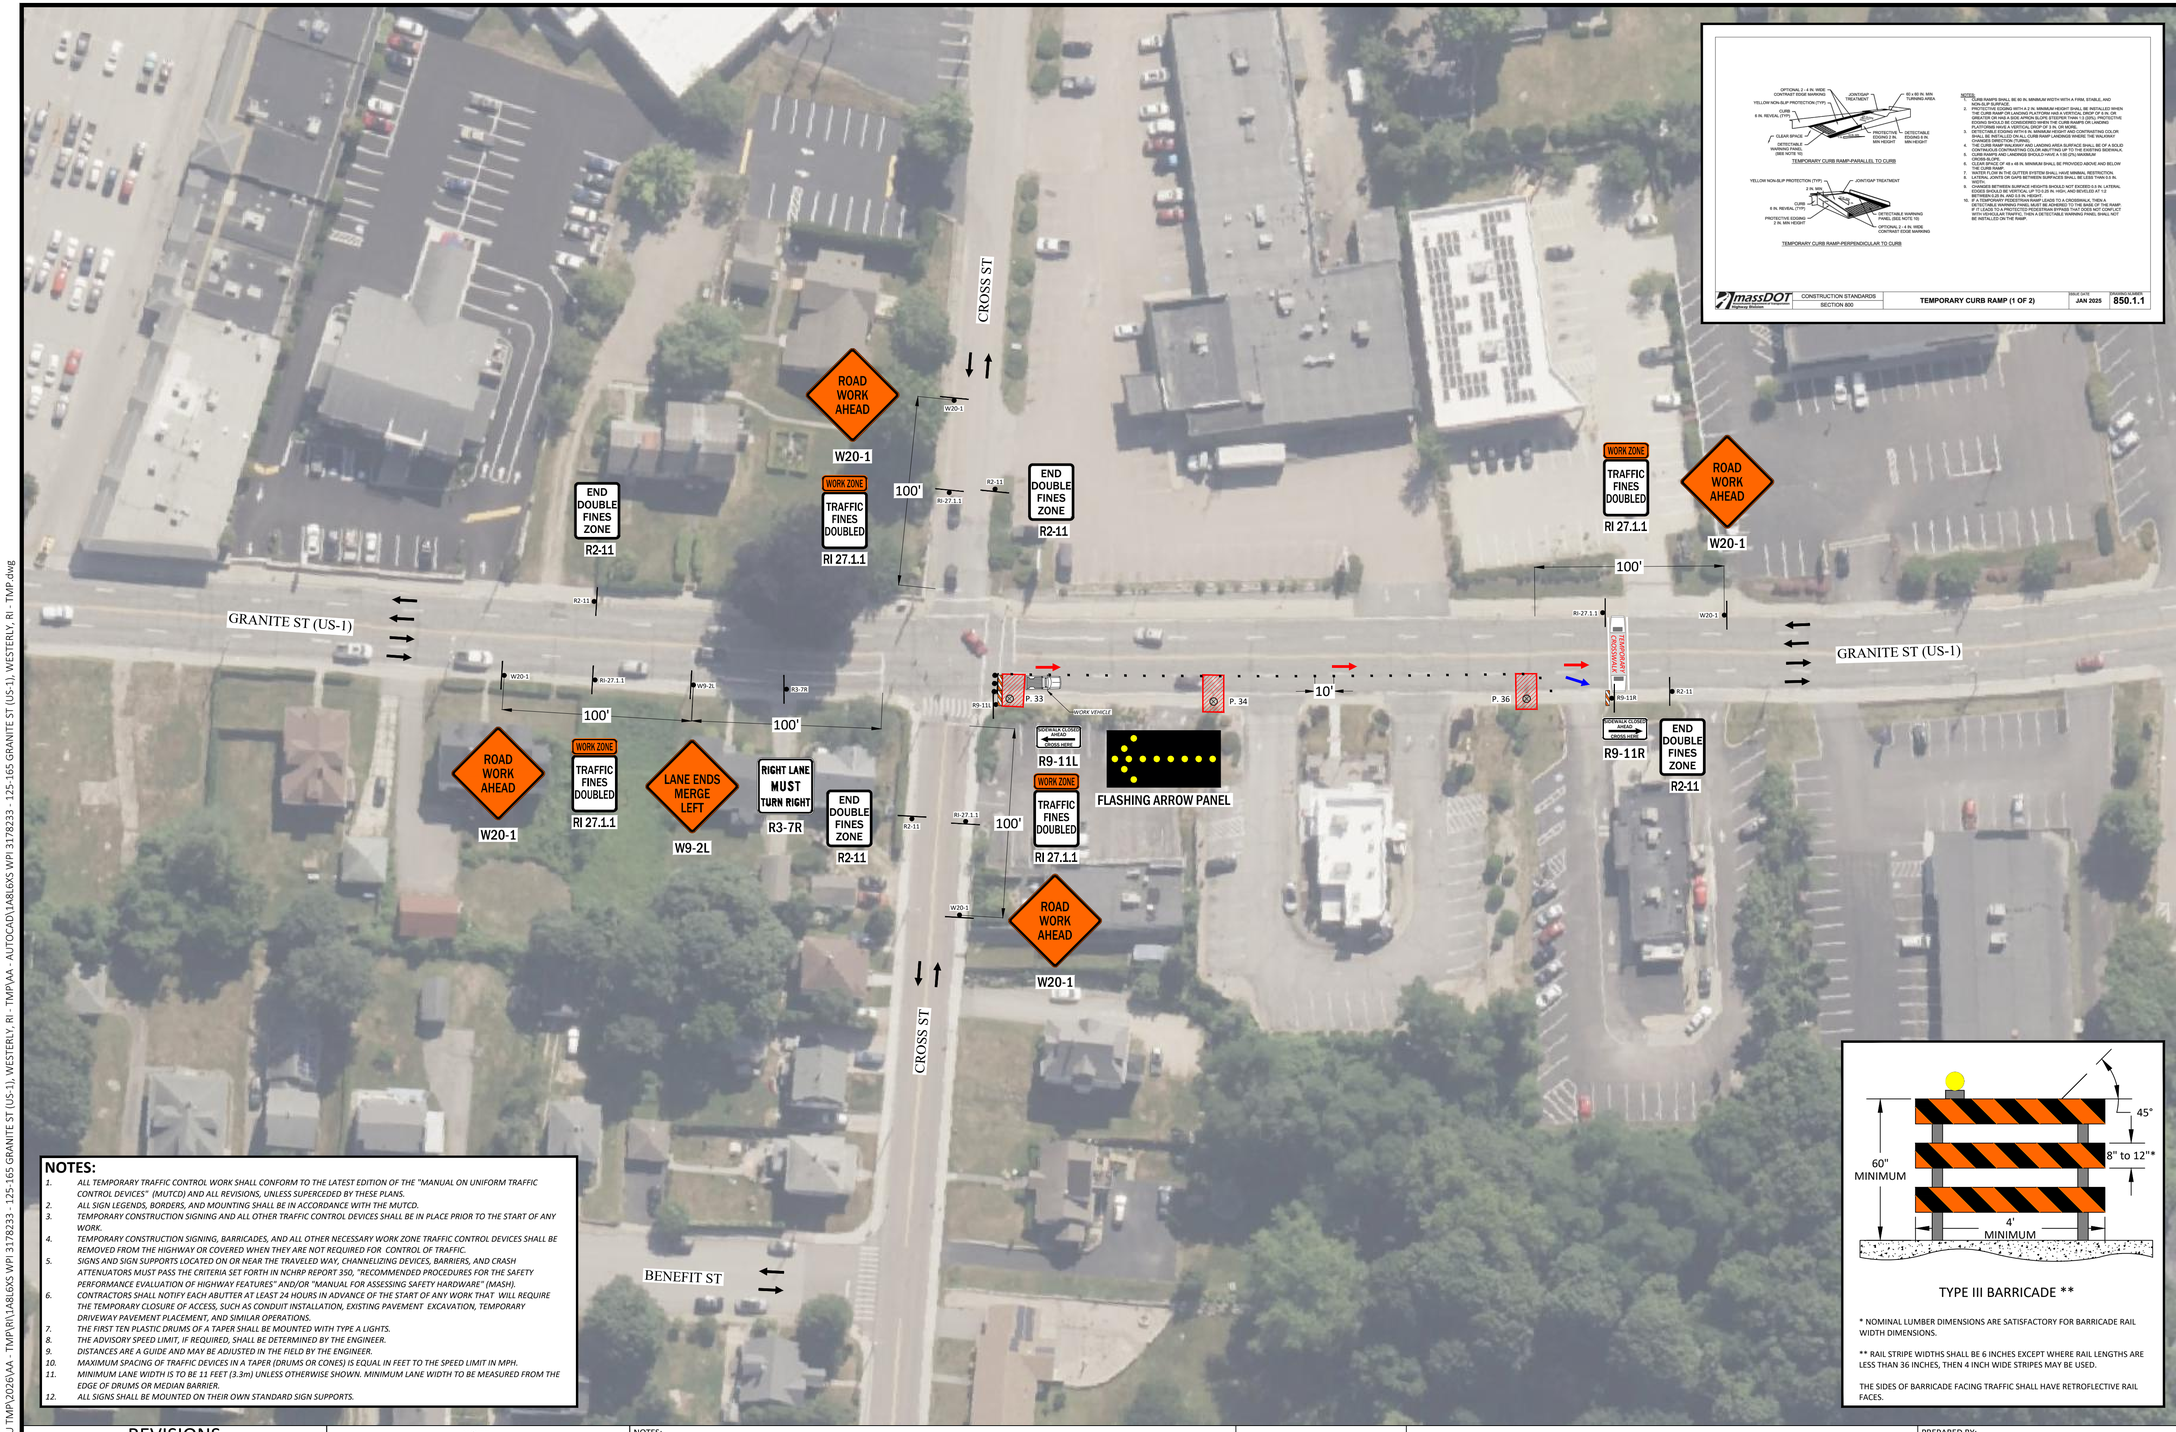


NOTES:


1. *ALL TEMPORARY TRAFFIC CONTROL WORK SHALL CONFORM TO THE LATEST EDITION OF THE "MANUAL ON UNIFORM TRAFFIC CONTROL DEVICES" (MUTCD) AND ALL REVISIONS, UNLESS SUPERCEDED BY THESE PLANS.*
2. *ALL SIGN LEGENDS, BORDERS, AND MOUNTING SHALL BE IN ACCORDANCE WITH THE MUTCD.*
3. *TEMPORARY CONSTRUCTION SIGNING AND ALL OTHER TRAFFIC CONTROL DEVICES SHALL BE IN PLACE PRIOR TO THE START OF ANY WORK.*
4. *TEMPORARY CONSTRUCTION SIGNING, BARRICADES, AND ALL OTHER NECESSARY WORK ZONE TRAFFIC CONTROL DEVICES SHALL BE REMOVED FROM THE HIGHWAY OR COVERED WHEN THEY ARE NOT REQUIRED FOR CONTROL OF TRAFFIC.*
5. *SIGNS AND SIGN SUPPORTS LOCATED ON OR NEAR THE TRAVELED WAY, CHANNELIZING DEVICES, BARRIERS, AND CRASH ATTENUATORS MUST PASS THE CRITERIA SET FORTH IN NCHRP REPORT 350, "RECOMMENDED PROCEDURES FOR THE SAFETY PERFORMANCE EVALUATION OF HIGHWAY FEATURES" AND/OR "MANUAL FOR ASSESSING SAFETY HARDWARE" (MASH).*
6. *CONTRACTORS SHALL NOTIFY EACH ABUTTER AT LEAST 24 HOURS IN ADVANCE OF THE START OF ANY WORK THAT WILL REQUIRE THE TEMPORARY CLOSURE OF ACCESS, SUCH AS CONDUIT INSTALLATION, EXISTING PAVEMENT EXCAVATION, TEMPORARY DRIVEWAY PAVEMENT PLACEMENT, AND SIMILAR OPERATIONS.*
7. *THE FIRST TEN PLASTIC DRUMS OF A TAPER SHALL BE MOUNTED WITH TYPE A LIGHTS.*
8. *THE ADVISORY SPEED LIMIT, IF REQUIRED, SHALL BE DETERMINED BY THE ENGINEER.*
9. *DISTANCES ARE A GUIDE AND MAY BE ADJUSTED IN THE FIELD BY THE ENGINEER.*
10. *MAXIMUM SPACING OF TRAFFIC DEVICES IN A TAPER (DRUMS OR CONES) IS EQUAL IN FEET TO THE SPEED LIMIT IN MPH.*
11. *MINIMUM LANE WIDTH IS TO BE 11 FEET (3.3m) UNLESS OTHERWISE SHOWN. MINIMUM LANE WIDTH TO BE MEASURED FROM THE EDGE OF DRUMS OR MEDIAN BARRIER.*
12. *ALL SIGNS SHALL BE MOUNTED ON THEIR OWN STANDARD SIGN SUPPORTS.*

TRAFFIC LEGEND

	WORK ZONE
	PROPOSED TRENCH
■	CHANNELIZING DEVICE (CONE)
◉	CHANNELIZING DEVICE (BARREL)
	SIGN
	POLICE DETAIL
	SINGLE PARKING METER
	DOUBLE PARKING METER
V	VARIABLE MESSAGE BOARD
	ARROW BOARD
	TYPE 3 BARRICADE
	HIGH LEVEL WARNING DEVICE
	CONSTRUCTION TRUCK
	TRUCK MOUNTED ATTENUATOR
	1 WAY STREET
	2 WAY STREET
	2 WAY TRAFFIC (WORK ZONE)
	TRAFFIC FLOW (WORK ZONE)
	TRAFFIC FLOW (WORK ZONE)
	TRAFFIC FLOW (WORK ZONE)
Ⓡ	EXISTING RIPTA BUS STOP
Ⓡ	RELOCATED RIPTA BUS STOP



CHANNELIZATION DEVICE DETAIL
TYPICAL
NOT TO SCALE



FREE STANDING
SELF SUPPORT SIGN
(TYPICAL)
(NOT TO SCALE)

PAGE 792
PER SEC. 6F.03
MUTCD 11th EDITION
DECEMBER 2023

TYPE III BARRICADE **

* NOMINAL LUMBER DIMENSIONS ARE SATISFACTORY FOR BARRICADE RAIL WIDTH DIMENSIONS.

** RAIL STRIPE WIDTHS SHALL BE 6 INCHES EXCEPT WHERE RAIL LENGTHS ARE LESS THAN 36 INCHES, THEN 4 INCH WIDE STRIPES MAY BE USED.

THE SIDES OF BARRICADE FACING TRAFFIC SHALL HAVE RETROFLECTIVE RAIL FACES.

REVISIONS

REV	DESCRIPTION	DATE
--	---	---

NOTE:
EXISTING UTILITIES SHOWN ARE APPROXIMATE AND NOT WARRANTED TO BE CORRECT. THE CONTRACTOR SHALL VERIFY THE LOCATION OF ALL PUBLIC AND PRIVATE UTILITIES PRIOR TO BEGINNING ANY EXCAVATION.

811 DigSafe MA RI NH VT
KNOW WHAT'S BELOW CALL BEFORE YOU DIG IT'S FREE AND IT'S THE LAW
CALL 811 OR 1-888-DIG-SAFE

NOTES:
- SPEED LIMIT 25 MPH AS OBSERVED IN THE FIELD.
- ALLOW BREAKS IN CHANNELIZATION DEVICES TO PERMIT DRIVEWAY ACCESS.

SCALE:
1"= 40 FEET
0 40 80 120 160

PREPARED BY:
PIKE TELECOM
21 Oxford Rd
Mansfield, MA 02048
www.piketelecom.com
1-508-337-7600

PREPARED FOR:
verizon

TITLE:
TRAFFIC MANAGEMENT PLAN - PHASE II
GRANITE ST (US-1)
WESTERLY, RI 02891

SURVEYED BY: PIKE TELECOM	PRINT NO: 2 OF 6
DRAWN BY: SHB	SCALE: 1" = 40'
DATE: 10/15/26	EWO: 1A8L6XS WPI 3178233

10/20/2026 N:\CADD\VERIZON BAU TMP\2026\AA - TMP\RI\1A8L6XS WPI 3178233 - 125-165 GRANITE ST (US-1), WESTERLY, RI - TMP.dwg

018150300411645

PHASE III

LONGVUE AVE

CROSS ST

JOHN ST

GRANITE ST (US-1)

ROAD WORK AHEAD W20-1

WORK ZONE TRAFFIC FINES DOUBLED RI 27.1.1

END DOUBLE FINES ZONE R2-11

RIGHT LANE CLOSED AHEAD W20-5R

R9-11L

R9-11R

W4-2R

SIDEWALK CLOSED R9-9

P. 37

P. 38

P. 38-50

100'

135'


115'

50'


10'

TRAFFIC LEGEND

	WORK ZONE
	PROPOSED TRENCH
■	CHANNELIZING DEVICE (CONE)
◉	CHANNELIZING DEVICE (BARREL)
	SIGN
	POLICE DETAIL
	SINGLE PARKING METER
	DOUBLE PARKING METER
V	VARIABLE MESSAGE BOARD
	ARROW BOARD
	TYPE 3 BARRICADE
	HIGH LEVEL WARNING DEVICE
	CONSTRUCTION TRUCK
	TRUCK MOUNTED ATTENUATOR
	1 WAY STREET
	2 WAY STREET
	2 WAY TRAFFIC (WORK ZONE)
	TRAFFIC FLOW (WORK ZONE)
	TRAFFIC FLOW (WORK ZONE)
	TRAFFIC FLOW (WORK ZONE)
Ⓡ	EXISTING RIPTA BUS STOP
Ⓡ	RELOCATED RIPTA BUS STOP



CHANNELIZATION DEVICE DETAIL
TYPICAL
NOT TO SCALE




TYPE III BARRICADE **

* NOMINAL LUMBER DIMENSIONS ARE SATISFACTORY FOR BARRICADE RAIL WIDTH DIMENSIONS.

** RAIL STRIPE WIDTHS SHALL BE 6 INCHES EXCEPT WHERE RAIL LENGTHS ARE LESS THAN 36 INCHES, THEN 4 INCH WIDE STRIPES MAY BE USED.

THE SIDES OF BARRICADE FACING TRAFFIC SHALL HAVE RETROFLECTIVE RAIL FACES.



FREE STANDING
SELF SUPPORT SIGN
(TYPICAL)
(NOT TO SCALE)

PAGE 792
PER SEC. 6F.03
MUTCD 11th EDITION
DECEMBER 2023

NOTES:

1. *ALL TEMPORARY TRAFFIC CONTROL WORK SHALL CONFORM TO THE LATEST EDITION OF THE "MANUAL ON UNIFORM TRAFFIC CONTROL DEVICES" (MUTCD) AND ALL REVISIONS, UNLESS SUPERCEDED BY THESE PLANS.*
2. *ALL SIGN LEGENDS, BORDERS, AND MOUNTING SHALL BE IN ACCORDANCE WITH THE MUTCD.*
3. *TEMPORARY CONSTRUCTION SIGNING AND ALL OTHER TRAFFIC CONTROL DEVICES SHALL BE IN PLACE PRIOR TO THE START OF ANY WORK.*
4. *TEMPORARY CONSTRUCTION SIGNING, BARRICADES, AND ALL OTHER NECESSARY WORK ZONE TRAFFIC CONTROL DEVICES SHALL BE REMOVED FROM THE HIGHWAY OR COVERED WHEN THEY ARE NOT REQUIRED FOR CONTROL OF TRAFFIC.*
5. *SIGNS AND SIGN SUPPORTS LOCATED ON OR NEAR THE TRAVELED WAY, CHANNELIZING DEVICES, BARRIERS, AND CRASH ATTENUATORS MUST PASS THE CRITERIA SET FORTH IN NCHRP REPORT 350, "RECOMMENDED PROCEDURES FOR THE SAFETY PERFORMANCE EVALUATION OF HIGHWAY FEATURES" AND/OR "MANUAL FOR ASSESSING SAFETY HARDWARE" (MASH).*
6. *CONTRACTORS SHALL NOTIFY EACH ABUTTER AT LEAST 24 HOURS IN ADVANCE OF THE START OF ANY WORK THAT WILL REQUIRE THE TEMPORARY CLOSURE OF ACCESS, SUCH AS CONDUIT INSTALLATION, EXISTING PAVEMENT EXCAVATION, TEMPORARY DRIVEWAY PAVEMENT PLACEMENT, AND SIMILAR OPERATIONS.*
7. *THE FIRST TEN PLASTIC DRUMS OF A TAPER SHALL BE MOUNTED WITH TYPE A LIGHTS.*
8. *THE ADVISORY SPEED LIMIT, IF REQUIRED, SHALL BE DETERMINED BY THE ENGINEER.*
9. *DISTANCES ARE A GUIDE AND MAY BE ADJUSTED IN THE FIELD BY THE ENGINEER.*
10. *MAXIMUM SPACING OF TRAFFIC DEVICES IN A TAPER (DRUMS OR CONES) IS EQUAL IN FEET TO THE SPEED LIMIT IN MPH.*
11. *MINIMUM LANE WIDTH IS TO BE 11 FEET (3.3m) UNLESS OTHERWISE SHOWN. MINIMUM LANE WIDTH TO BE MEASURED FROM THE EDGE OF DRUMS OR MEDIAN BARRIER.*
12. *ALL SIGNS SHALL BE MOUNTED ON THEIR OWN STANDARD SIGN SUPPORTS.*

REVISIONS

REV	DESCRIPTION	DATE
--	---	---

NOTE:
EXISTING UTILITIES SHOWN ARE APPROXIMATE AND NOT WARRANTED TO BE CORRECT. THE CONTRACTOR SHALL VERIFY THE LOCATION OF ALL PUBLIC AND PRIVATE UTILITIES PRIOR TO BEGINNING ANY EXCAVATION.

811 DigSafe MA RI NH VT

KNOW WHAT'S BELOW CALL BEFORE YOU DIG IT'S FREE AND IT'S THE LAW

CALL 811 OR 1-888-DIG-SAFE

NOTES:
- SPEED LIMIT 25 MPH AS OBSERVED IN THE FIELD.
- ALLOW BREAKS IN CHANNELIZATION DEVICES TO PERMIT DRIVEWAY ACCESS.

SCALE:

1"= 50 FEET

0 50 100 150 200

PREPARED BY:

PIKE TELECOM
21 Oxford Rd
Mansfield, MA 02048
www.piketelecom.com
1-508-337-7600

PREPARED FOR:

verizon

TITLE:

TRAFFIC MANAGEMENT PLAN - PHASE III
GRANITE ST (US-1)
WESTERLY, RI 02891


SURVEYED BY: PIKE TELECOM	PRINT NO: 3 OF 6
DRAWN BY: SHB	SCALE: 1" = 50'
DATE: 10/15/26	EWO: 1A8L6XS WPI 3178233

10/20/2026 N:\CADD\VERIZON BAU TMP\2026\AA - TMP\RI\1A8L6XS WPI 3178233 - 125-165 GRANITE ST (US-1), WESTERLY, RI - TMP.dwg


018150300411645

PHASE IV

TRAFFIC LEGEND	
	WORK ZONE
	PROPOSED TRENCH
■	CHANNELIZING DEVICE (CONE)
◉	CHANNELIZING DEVICE (BARREL)
	SIGN
	POLICE DETAIL
	SINGLE PARKING METER
	DOUBLE PARKING METER
V	VARIABLE MESSAGE BOARD
	ARROW BOARD
	TYPE 3 BARRICADE
	HIGH LEVEL WARNING DEVICE
	CONSTRUCTION TRUCK
	TRUCK MOUNTED ATTENUATOR
	1 WAY STREET
	2 WAY STREET
	2 WAY TRAFFIC (WORK ZONE)
	TRAFFIC FLOW (WORK ZONE)
	TRAFFIC FLOW (WORK ZONE)
	TRAFFIC FLOW (WORK ZONE)
Ⓡ	EXISTING RIPTA BUS STOP
Ⓡ	RELOCATED RIPTA BUS STOP




CHANNELIZATION DEVICE DETAIL
TYPICAL
NOT TO SCALE



FREE STANDING
SELF SUPPORT SIGN
(TYPICAL)
(NOT TO SCALE)

PAGE 792
PER SEC. 6F.03
MUTCD 11th EDITION
DECEMBER 2023



TYPE III BARRICADE **

* NOMINAL LUMBER DIMENSIONS ARE SATISFACTORY FOR BARRICADE RAIL WIDTH DIMENSIONS.

** RAIL STRIPE WIDTHS SHALL BE 6 INCHES EXCEPT WHERE RAIL LENGTHS ARE LESS THAN 36 INCHES, THEN 4 INCH WIDE STRIPES MAY BE USED.

THE SIDES OF BARRICADE FACING TRAFFIC SHALL HAVE RETROFLECTIVE RAIL FACES.

GRANITE ST (US-1)

JOHN ST

CABIN CT

END DOUBLE FINES ZONE R2-11

WORK ZONE TRAFFIC FINES DOUBLED RI 27.1.1

ROAD WORK AHEAD W20-1

90' 100' 100' 115' 10' 110' 90'

RIGHT LANE CLOSED AHEAD W20-5R

W4-2R

WORK VEHICLE

SIDEWALK CLOSED R9-9

P. 39

SIDEWALK CLOSED AHEAD CROSS HERE R9-11R

NOTES:

1. *ALL TEMPORARY TRAFFIC CONTROL WORK SHALL CONFORM TO THE LATEST EDITION OF THE "MANUAL ON UNIFORM TRAFFIC CONTROL DEVICES" (MUTCD) AND ALL REVISIONS, UNLESS SUPERCEDED BY THESE PLANS.*
2. *ALL SIGN LEGENDS, BORDERS, AND MOUNTING SHALL BE IN ACCORDANCE WITH THE MUTCD.*
3. *TEMPORARY CONSTRUCTION SIGNING AND ALL OTHER TRAFFIC CONTROL DEVICES SHALL BE IN PLACE PRIOR TO THE START OF ANY WORK.*
4. *TEMPORARY CONSTRUCTION SIGNING, BARRICADES, AND ALL OTHER NECESSARY WORK ZONE TRAFFIC CONTROL DEVICES SHALL BE REMOVED FROM THE HIGHWAY OR COVERED WHEN THEY ARE NOT REQUIRED FOR CONTROL OF TRAFFIC.*
5. *SIGNS AND SIGN SUPPORTS LOCATED ON OR NEAR THE TRAVELED WAY, CHANNELIZING DEVICES, BARRIERS, AND CRASH ATTENUATORS MUST PASS THE CRITERIA SET FORTH IN NCHRP REPORT 350, "RECOMMENDED PROCEDURES FOR THE SAFETY PERFORMANCE EVALUATION OF HIGHWAY FEATURES" AND/OR "MANUAL FOR ASSESSING SAFETY HARDWARE" (MASH).*
6. *CONTRACTORS SHALL NOTIFY EACH ABUTTER AT LEAST 24 HOURS IN ADVANCE OF THE START OF ANY WORK THAT WILL REQUIRE THE TEMPORARY CLOSURE OF ACCESS, SUCH AS CONDUIT INSTALLATION, EXISTING PAVEMENT EXCAVATION, TEMPORARY DRIVEWAY PAVEMENT PLACEMENT, AND SIMILAR OPERATIONS.*
7. *THE FIRST TEN PLASTIC DRUMS OF A TAPER SHALL BE MOUNTED WITH TYPE A LIGHTS.*
8. *THE ADVISORY SPEED LIMIT, IF REQUIRED, SHALL BE DETERMINED BY THE ENGINEER.*
9. *DISTANCES ARE A GUIDE AND MAY BE ADJUSTED IN THE FIELD BY THE ENGINEER.*
10. *MAXIMUM SPACING OF TRAFFIC DEVICES IN A TAPER (DRUMS OR CONES) IS EQUAL IN FEET TO THE SPEED LIMIT IN MPH.*
11. *MINIMUM LANE WIDTH IS TO BE 11 FEET (3.3m) UNLESS OTHERWISE SHOWN. MINIMUM LANE WIDTH TO BE MEASURED FROM THE EDGE OF DRUMS OR MEDIAN BARRIER.*
12. *ALL SIGNS SHALL BE MOUNTED ON THEIR OWN STANDARD SIGN SUPPORTS.*

REVISIONS

REV	DESCRIPTION	DATE
--	---	---

NOTE:
EXISTING UTILITIES SHOWN ARE APPROXIMATE AND NOT WARRANTED TO BE CORRECT. THE CONTRACTOR SHALL VERIFY THE LOCATION OF ALL PUBLIC AND PRIVATE UTILITIES PRIOR TO BEGINNING ANY EXCAVATION.

811 DigSafe MA ME NH RI VT

KNOW WHAT'S BELOW
CALL BEFORE YOU DIG
IT'S FREE AND IT'S THE LAW

CALL 811 OR 1-888-DIG-SAFE

NOTES:
- SPEED LIMIT 25 MPH AS OBSERVED IN THE FIELD.
- ALLOW BREAKS IN CHANNELIZATION DEVICES TO PERMIT DRIVEWAY ACCESS.

SCALE:

1"= 40 FEET

0 40 80 120 160

PREPARED BY:

PIKE TELECOM
21 Oxford Rd
Mansfield, MA 02048
www.piketelecom.com
1-508-337-7600

PREPARED FOR:

verizon

TITLE:

TRAFFIC MANAGEMENT PLAN - PHASE IV
GRANITE ST (US-1)
WESTERLY, RI 02891

SURVEYED BY: PIKE TELECOM	PRINT NO: 4 OF 6
DRAWN BY: SHB	SCALE: 1" = 40'
DATE: 10/15/26	EWO: 1A8L6XS WPI 3178233


10/20/2026 N:\CADD\VERIZON BAU TMP\2026\AA - TMP\RI\1A8L6XS WPI 3178233 - 125-165 GRANITE ST (US-1), WESTERLY, RI - TMP.dwg

018150300411645

PHASE V


NOTES:

1. ALL TEMPORARY TRAFFIC CONTROL WORK SHALL CONFORM TO THE LATEST EDITION OF THE "MANUAL ON UNIFORM TRAFFIC CONTROL DEVICES" (MUTCD) AND ALL REVISIONS, UNLESS SUPERCEDED BY THESE PLANS.
2. ALL SIGN LEGENDS, BORDERS, AND MOUNTING SHALL BE IN ACCORDANCE WITH THE MUTCD.
3. TEMPORARY CONSTRUCTION SIGNING AND ALL OTHER TRAFFIC CONTROL DEVICES SHALL BE IN PLACE PRIOR TO THE START OF ANY WORK.
4. TEMPORARY CONSTRUCTION SIGNING, BARRICADES, AND ALL OTHER NECESSARY WORK ZONE TRAFFIC CONTROL DEVICES SHALL BE REMOVED FROM THE HIGHWAY OR COVERED WHEN THEY ARE NOT REQUIRED FOR CONTROL OF TRAFFIC.
5. SIGNS AND SIGN SUPPORTS LOCATED ON OR NEAR THE TRAVELED WAY, CHANNELIZING DEVICES, BARRIERS, AND CRASH ATTENUATORS MUST PASS THE CRITERIA SET FORTH IN NCHRP REPORT 350, "RECOMMENDED PROCEDURES FOR THE SAFETY PERFORMANCE EVALUATION OF HIGHWAY FEATURES" AND/OR "MANUAL FOR ASSESSING SAFETY HARDWARE" (MASH).
6. CONTRACTORS SHALL NOTIFY EACH ABUTTER AT LEAST 24 HOURS IN ADVANCE OF THE START OF ANY WORK THAT WILL REQUIRE THE TEMPORARY CLOSURE OF ACCESS, SUCH AS CONDUIT INSTALLATION, EXISTING PAVEMENT EXCAVATION, TEMPORARY DRIVEWAY PAVEMENT PLACEMENT, AND SIMILAR OPERATIONS.
7. THE FIRST TEN PLASTIC DRUMS OF A TAPER SHALL BE MOUNTED WITH TYPE A LIGHTS.
8. THE ADVISORY SPEED LIMIT, IF REQUIRED, SHALL BE DETERMINED BY THE ENGINEER.
9. DISTANCES ARE A GUIDE AND MAY BE ADJUSTED IN THE FIELD BY THE ENGINEER.
10. MAXIMUM SPACING OF TRAFFIC DEVICES IN A TAPER (DRUMS OR CONES) IS EQUAL IN FEET TO THE SPEED LIMIT IN MPH.
11. MINIMUM LANE WIDTH IS TO BE 11 FEET (3.3m) UNLESS OTHERWISE SHOWN. MINIMUM LANE WIDTH TO BE MEASURED FROM THE EDGE OF DRUMS OR MEDIAN BARRIER.
12. ALL SIGNS SHALL BE MOUNTED ON THEIR OWN STANDARD SIGN SUPPORTS.

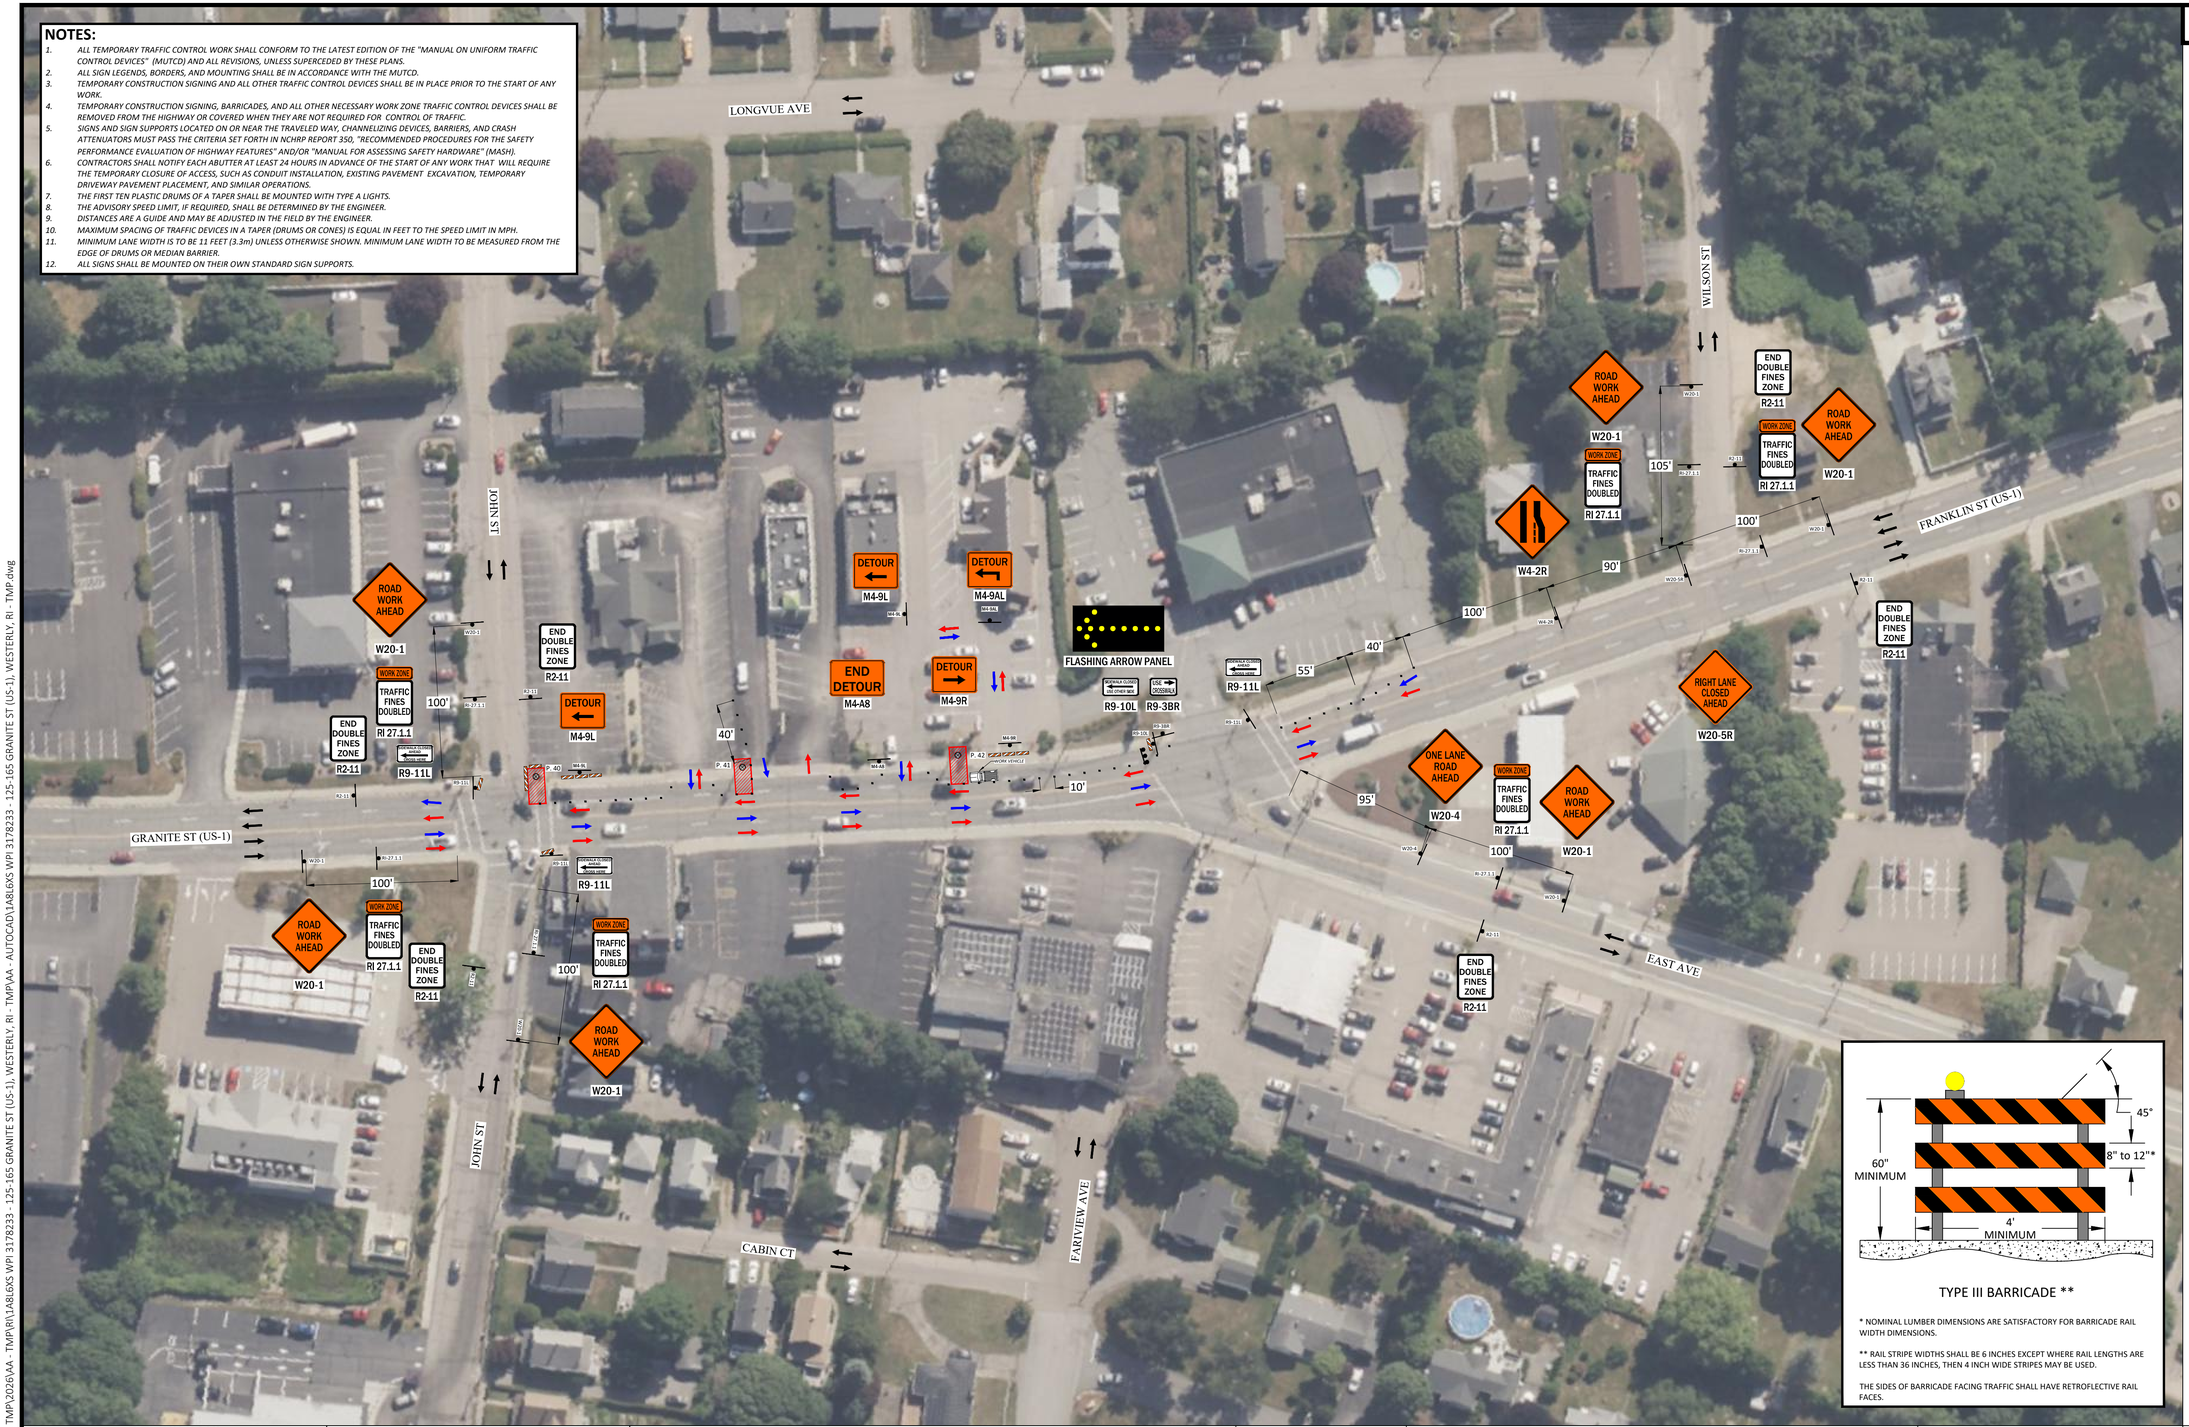


TRAFFIC LEGEND

	WORK ZONE
	PROPOSED TRENCH
■	CHANNELIZING DEVICE (CONE)
◉	CHANNELIZING DEVICE (BARREL)
	SIGN
	POLICE DETAIL
	SINGLE PARKING METER
	DOUBLE PARKING METER
V	VARIABLE MESSAGE BOARD
	ARROW BOARD
	TYPE 3 BARRICADE
	HIGH LEVEL WARNING DEVICE
	CONSTRUCTION TRUCK
	TRUCK MOUNTED ATTENUATOR
	1 WAY STREET
	2 WAY STREET
	2 WAY TRAFFIC (WORK ZONE)
	TRAFFIC FLOW (WORK ZONE)
	TRAFFIC FLOW (WORK ZONE)
	TRAFFIC FLOW (WORK ZONE)
Ⓡ	EXISTING RIPTA BUS STOP
Ⓡ	RELOCATED RIPTA BUS STOP



CHANNELIZATION DEVICE DETAIL
TYPICAL
NOT TO SCALE



FREE STANDING
SELF SUPPORT SIGN
(TYPICAL)
(NOT TO SCALE)

TYPE III BARRICADE **

* NOMINAL LUMBER DIMENSIONS ARE SATISFACTORY FOR BARRICADE RAIL WIDTH DIMENSIONS.

** RAIL STRIPE WIDTHS SHALL BE 6 INCHES EXCEPT WHERE RAIL LENGTHS ARE LESS THAN 36 INCHES, THEN 4 INCH WIDE STRIPES MAY BE USED.

THE SIDES OF BARRICADE FACING TRAFFIC SHALL HAVE RETROFLECTIVE RAIL FACES.

PAGE 792
PER SEC. 6F.03
MUTCD 11th EDITION
DECEMBER 2023

REVISIONS		
REV	DESCRIPTION	DATE
--	---	---

NOTE:
EXISTING UTILITIES SHOWN ARE APPROXIMATE AND NOT WARRANTED TO BE CORRECT. THE CONTRACTOR SHALL VERIFY THE LOCATION OF ALL PUBLIC AND PRIVATE UTILITIES PRIOR TO BEGINNING ANY EXCAVATION.

811 DigSafe MA RI NH CT VT
KNOW WHAT'S BELOW CALL BEFORE YOU DIG IT'S FREE AND IT'S THE LAW
CALL 811 OR 1-888-DIG-SAFE

NOTES:
- SPEED LIMIT 25 MPH AS OBSERVED IN THE FIELD.
- ALLOW BREAKS IN CHANNELIZATION DEVICES TO PERMIT DRIVEWAY ACCESS.

SCALE:
1"= 50 FEET
0 50 100 150 200

PREPARED BY:
PIKE TELECOM
21 Oxford Rd
Mansfield, MA 02048
www.piketelecom.com
1-508-337-7600

PREPARED FOR:
verizon

TITLE:
TRAFFIC MANAGEMENT PLAN - PHASE V
GRANITE ST (US-1)
WESTERLY, RI 02891


SURVEYED BY: PIKE TELECOM	PRINT NO: 5 OF 6
DRAWN BY: SHB	SCALE: 1" = 50'
DATE: 10/15/26	EWO: 1A8L6XS WPI 3178233

10/20/2026 N:\CADD\VERIZON BAU TMP\2026\AA - TMP\R\1A8L6XS WPI 3178233 - 125-165 GRANITE ST (US-1), WESTERLY, RI - TMP\AA - AUTOCAD\1A8L6XS WPI 3178233 - 125-165 GRANITE ST (US-1), WESTERLY, RI - TMP.dwg


018150300411645

PHASE VI

TRAFFIC LEGEND	
	WORK ZONE
	PROPOSED TRENCH
	CHANNELIZING DEVICE (CONE)
	CHANNELIZING DEVICE (BARREL)
	SIGN
	POLICE DETAIL
	SINGLE PARKING METER
	DOUBLE PARKING METER
V	VARIABLE MESSAGE BOARD
	ARROW BOARD
	TYPE 3 BARRICADE
	HIGH LEVEL WARNING DEVICE
	CONSTRUCTION TRUCK
	TRUCK MOUNTED ATTENUATOR
	1 WAY STREET
	2 WAY STREET
	2 WAY TRAFFIC (WORK ZONE)
	TRAFFIC FLOW (WORK ZONE)
	TRAFFIC FLOW (WORK ZONE)
	TRAFFIC FLOW (WORK ZONE)
Ⓡ	EXISTING RIPTA BUS STOP
Ⓡ	RELOCATED RIPTA BUS STOP




CHANNELIZATION DEVICE DETAIL
TYPICAL
NOT TO SCALE



FREE STANDING
SELF SUPPORT SIGN
(TYPICAL)
(NOT TO SCALE)

PAGE 792
PER SEC. 6F.03
MUTCD 11th EDITION
DECEMBER 2023

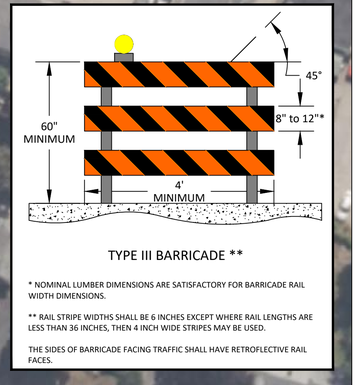

TYPE III BARRICADE **

* NOMINAL LUMBER DIMENSIONS ARE SATISFACTORY FOR BARRICADE RAIL WIDTH DIMENSIONS.

** RAIL STRIPE WIDTHS SHALL BE 6 INCHES EXCEPT WHERE RAIL LENGTHS ARE LESS THAN 36 INCHES, THEN 4 INCH WIDE STRIPES MAY BE USED.

THE SIDES OF BARRICADE FACING TRAFFIC SHALL HAVE RETROFLECTIVE RAIL FACES.

NOTES:

1. *ALL TEMPORARY TRAFFIC CONTROL WORK SHALL CONFORM TO THE LATEST EDITION OF THE "MANUAL ON UNIFORM TRAFFIC CONTROL DEVICES" (MUTCD) AND ALL REVISIONS, UNLESS SUPERCEDED BY THESE PLANS.*
2. *ALL SIGN LEGENDS, BORDERS, AND MOUNTING SHALL BE IN ACCORDANCE WITH THE MUTCD.*
3. *TEMPORARY CONSTRUCTION SIGNING AND ALL OTHER TRAFFIC CONTROL DEVICES SHALL BE IN PLACE PRIOR TO THE START OF ANY WORK.*
4. *TEMPORARY CONSTRUCTION SIGNING, BARRICADES, AND ALL OTHER NECESSARY WORK ZONE TRAFFIC CONTROL DEVICES SHALL BE REMOVED FROM THE HIGHWAY OR COVERED WHEN THEY ARE NOT REQUIRED FOR CONTROL OF TRAFFIC.*
5. *SIGNS AND SIGN SUPPORTS LOCATED ON OR NEAR THE TRAVELED WAY, CHANNELIZING DEVICES, BARRIERS, AND CRASH ATTENUATORS MUST PASS THE CRITERIA SET FORTH IN NCHRP REPORT 350, "RECOMMENDED PROCEDURES FOR THE SAFETY PERFORMANCE EVALUATION OF HIGHWAY FEATURES" AND/OR "MANUAL FOR ASSESSING SAFETY HARDWARE" (MASH).*
6. *CONTRACTORS SHALL NOTIFY EACH ABUTTER AT LEAST 24 HOURS IN ADVANCE OF THE START OF ANY WORK THAT WILL REQUIRE THE TEMPORARY CLOSURE OF ACCESS, SUCH AS CONDUIT INSTALLATION, EXISTING PAVEMENT EXCAVATION, TEMPORARY DRIVEWAY PAVEMENT PLACEMENT, AND SIMILAR OPERATIONS.*
7. *THE FIRST TEN PLASTIC DRUMS OF A TAPER SHALL BE MOUNTED WITH TYPE A LIGHTS.*
8. *THE ADVISORY SPEED LIMIT, IF REQUIRED, SHALL BE DETERMINED BY THE ENGINEER.*
9. *DISTANCES ARE A GUIDE AND MAY BE ADJUSTED IN THE FIELD BY THE ENGINEER.*
10. *MAXIMUM SPACING OF TRAFFIC DEVICES IN A TAPER (DRUMS OR CONES) IS EQUAL IN FEET TO THE SPEED LIMIT IN MPH.*
11. *MINIMUM LANE WIDTH IS TO BE 11 FEET (3.3m) UNLESS OTHERWISE SHOWN. MINIMUM LANE WIDTH TO BE MEASURED FROM THE EDGE OF DRUMS OR MEDIAN BARRIER.*
12. *ALL SIGNS SHALL BE MOUNTED ON THEIR OWN STANDARD SIGN SUPPORTS.*

REVISIONS

REV	DESCRIPTION	DATE
--	---	---

NOTE:
EXISTING UTILITIES SHOWN ARE APPROXIMATE AND NOT WARRANTED TO BE CORRECT. THE CONTRACTOR SHALL VERIFY THE LOCATION OF ALL PUBLIC AND PRIVATE UTILITIES PRIOR TO BEGINNING ANY EXCAVATION.

811 DigSafe MA ME NH RI VT
KNOW WHAT'S BELOW CALL BEFORE YOU DIG IT'S FREE AND IT'S THE LAW
CALL 811 OR 1-888-DIG-SAFE

NOTES:
- SPEED LIMIT 25 MPH AS OBSERVED IN THE FIELD.
- ALLOW BREAKS IN CHANNELIZATION DEVICES TO PERMIT DRIVEWAY ACCESS.

SCALE:
1"= 40 FEET
0 40 80 120 160

PREPARED BY:
PIKE TELECOM
21 Oxford Rd
Mansfield, MA 02048
www.piketelecom.com
1-508-337-7600

PREPARED FOR:
verizon

TITLE:
TRAFFIC MANAGEMENT PLAN - PHASE VI
GRANITE ST (US-1)
WESTERLY, RI 02891

SURVEYED BY: PIKE TELECOM	PRINT NO: 6 OF 6
DRAWN BY: SHB	SCALE: 1" = 40'
DATE: 10/15/26	EWO: 1A8L6XS WPI 3178233

10/20/2026 N:\CAD\VERIZON BAU\TMP\2026\AA - TMP\R\1A8L6XS WPI 3178233 - 125-165 GRANITE ST (US-1), WESTERLY, RI - TMP.dwg

018150300411645
